

Mr. Bailey Trigg
Project Manager
The APP Group
Level 2, 426 King Street
Newcastle NSW 2300

15 August 2025

Subject: University of Newcastle, City Campus Student Accommodation - Staging Report

Dear Mr Trigg,

I refer to the *Staging Report University of Newcastle City Campus Student Accommodation* (Job SN114, Revision D, dated 11 August 2025, prepared by The APP Group) ('the Report'), submitted in accordance with Schedule 2, Condition A20 of the University of Newcastle City Campus Stage 1B, including a nine-storey building (known as Building B) for the purpose of student campus accommodation and ground floor retail Development Consent (SSD-61618229). I also acknowledge your response to the Department's review comments and request for additional information.

The Department has carefully reviewed the Report and is satisfied that it meets the requirements of Condition A20.


Please ensure that:

- any Aboriginal archaeology salvage works are completed prior to construction impacts per the construction programme; and
- the Locomotive Turntable exclusion zone is maintained for the duration of construction, in accordance with Condition C41.

You are reminded that if there are any inconsistencies between the Report and the conditions of consent, the conditions prevail.

Please ensure that you make the Report publicly available on the project website at your earliest convenience.

Yours sincerely,



Michael Doyle
A/Team Leader, Regional Assessments
As nominee of the Planning Secretary

11 August 2025

Jane Flanagan
Senior Planner
Key Sites & Regional Assessments
Department of Planning and Environment
4 Parramatta Square
12 Darcy Street PARRAMATTA

Dear Ms Flanagan,

Re: SSD-61618229-PA-5 City Campus Student Accommodation Staging Report

APP have reviewed your Request for Information dated 11th of July 2025 and provide the following response:

RFI – 11/08/2025

Please submit a revised version which corrects the references to the following duplicate figures: two different versions of Figure 5 are on pages 12 and 13; and two different versions of Figure 6 are on pages 11 and 14).

Please also update the date and revision number of the Report, accordingly.

Response – 11/08/2025

Please refer to the attached Revision D of the Staging Report as per your request.

Should further information be required please don't hesitate to contact the undersigned.

Yours sincerely,




Bailey Trigg
Project Manager
0435 447 069

Attachment A – Revised Staging Report Revision D

STAGING REPORT

PROJECT: UNIVERSITY OF NEWCASTLE CITY CAMPUS STUDENT
ACCOMMODATION
JOB NO: SN114



Rev: D 11/0825

Uncontrolled Document in Hard Copy
Copies shall not be made without the written
permission of Hansen Yuncken Project Manager

Contents

1	Distribution & Authorisation.....	3
1.1	Version Control	3
1.2	Authorisation Record.....	3
2	Objective	4
3	Introduction	5
3.1	Project Overview	5
3.2	Site Plan.....	6
4	Staged Construction Certificates	7
	CC Overview:	7
4.1	Construction Certificate 1 – Groundworks, In-ground services & Substructure.....	7
4.2	Construction Certificate 2 – Superstructure.....	9
4.3	Construction Certificate 3 – Façade	10
4.4	Construction Certificate 4 – Services and Finishes / Fitout	12
4.5	Construction Certificate 5 – Balance of Works	12
5	Operation	15
6	Construction Risk Management.....	16
7	Conclusion	17
8	Appendices.....	18
8.1	SSDA Matrix.....	19
8.2	Construction Programme	20

Figure List

Figure 1: University of Newcastle City Campus development overview.

Figure 2: Site Establishment Overview

Figure 3a: Overview of CC1 works.

Figure 3b: Footing Plan

Figure 4a: Ground Plan Structural Overview

Figure 4b: Roof Plan Structural Overview

Figure 5: Overview of façade elevations (plan view)

Figure 6: Overview of façade elevations (elevation view)

Figure 7: Overview of CC4 works.

Figure 8: Ground Floor Zone 1 Public Domain and landscaping works

Figure 9: Ground Floor Zone 2 landscaping works.

Figure 10: Level 1 podium landscaping works

1 Distribution & Authorisation

1.1 Version Control

Version	Prepared by Name	Sign	Date
Revision A - Draft	Stephanie Ganis		23/5/25
Revision B – Final	Stephanie Ganis		5/6/25
Revision C – Final – Update Revision and SSDA Matrix	Tom Clark		01/08/2025
Revision D – Final – Figure List and Figure Numbering Updated	Tom Clark		11/08/2025

1.2 Authorisation Record

Version	Prepared by Name	Sign	Date Authorised
Revision A - Draft	Stephanie Ganis		
Revision B – Final	Stephanie Ganis		5/6/25
Revision C – Final – Update Revision and SSDA Matrix	Tom Clark		01/08/2025
Revision D – Final – Figure List and Figure Numbering Updated	Tom Clark		11/08/2025

2 Objective

This report has been prepared to satisfy SSDA Condition #A20 – Staging Report. The condition reads as follows:

The project may be constructed and operated in stages. Where compliance with conditions is required to be staged due to staged construction or operation, a Staging Report (for either or both construction and operation as the case may be) must be prepared and submitted to the satisfaction of the Planning Secretary. The Staging Report must be submitted to the Planning Secretary no later than one month before the commencement of construction of the first of the proposed stages of construction (or if only staged operation is proposed, one month before the commencement of operation of the first of the proposed stages of operation).

This staging report will outline the following:

- The works to be completed under each stage (or construction certificate),
- Site establishment layout
- Timeframe for each stage / CC,
- Operational impacts and risk management

3 Introduction

3.1 Project Overview

This project forms part of the overarching University of Newcastle City Campus development, which includes a series of lots situated between Honeysuckle Drive and Civic Lane in Newcastle CBD. The overarching development will be completed over multiple stages and includes the following buildings:

- Stage 1A
 - o Building A1
- Stage 1B
 - o **Building B**
- Stage 2
 - o Building A2
- Stage 3
 - o Building C
- Stage 4
 - o Building D, E & F

This project specifically refers to **Building B**. This stage (Stage 1b), represents the next step in delivering the vision for the University's City Campus, and will build on the University's historical and current presence (University House, Northumberland House, Conservatorium of Music, NUspace and Q Building) in the Newcastle CBD.



Figure 1: University of Newcastle City Campus development overview.

The project works for Building B include:

- Site grading and removal of existing vegetation

- Construction of a nine storey building (building B) to be used for campus student accommodation and retail.
- Maximum gross floor area (GFA) of 10,765m², comprising of:
 - o Approximately 130m² of retail floor space at ground level,
 - o Approximately 683m² of communal residential amenity facilities at ground level, and
 - o Approximately 9,520m² of student accommodation including a total of 445 beds
- End of trip facilities, including 90 bicycle spaces and back of house amenities; and
- Associated landscaping and public domain work

3.2 Site Plan

The below Figure 2 indicates the general site establishment plan, outlining vehicle access points, site facilities, crange and traffic control provisions. The site office, amenities and contractor parking area shall remain in the designated area shown below throughout the duration of construction works.

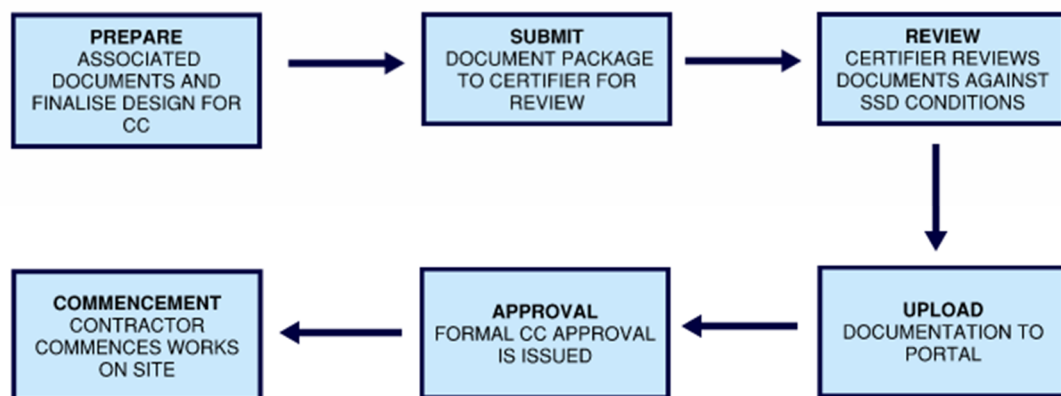


Figure 2: Site Establishment Overview

4 Staged Construction Certificates

CC Overview:

The below Construction Certificate (CC) Staging methodology has been determined following the review of the required design packages and the duration of the associated works packages. This aims to ensure appropriate design work and the required documentation is prepared in advance of submitting and commencing works under a particular CC. The process for each CC is as follows:



4.1 Construction Certificate 1 – Groundworks, In-ground services & Substructure

The specific works included under this CC include:

- Bulk and detailed excavation
- Piling & Footings
- In ground services and authority connections

The documentation for this CC will be prepared by Hansen Yuncken and the consultant design team and subcontractors. CC documentation for this phase will be collated in June 2025, with anticipated approval by July 2025. All works under this CC will be completed from July – October 2025. The timeline for this CC is as follows:

- Late June 2025
 - CC1 documentation to be finalised for PCA Review
- July 2025
 - Anticipated approval of CC1.
- July 2025 – October 2025
 - Duration of all groundworks including bulk earthworks, foundation piles and acid sulphate soil remediation.
- August 2025 – September 2025
 - Duration of lift pit structural works, OSD tank, Worth Place services works including footings and waterproofing
- August 2025 – October 2025
 - Incoming services works including stormwater reticulation and connection to pits, connection of sewer to existing, electrical services reticulation, installation of new fire hydrants and fire booster and connection to existing network.

Refer to Figure 3a and 3b below for the overview of works under CC1.

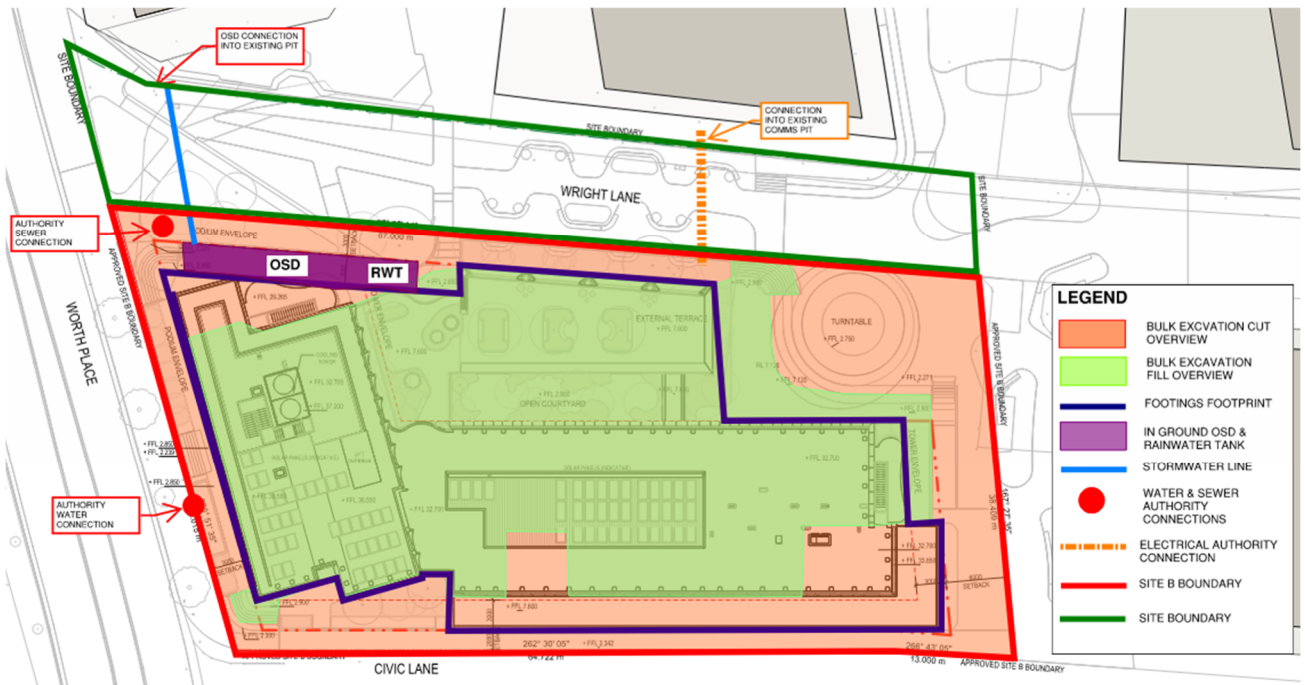


Figure 3a: Overview of CC1 works.



Figure 3b: Footing Plan

4.2 Construction Certificate 2 – Superstructure

The specific works included under this CC include:

- Superstructure from ground level to roof / plant

The documentation for this CC will be prepared by Hansen Yuncken and the consultant design team and subcontractors. CC documentation for this phase will be collated in August 2025, with anticipated approval by late August 2025. All works under this CC will be completed from September – June 2026. The timeline for this CC is as follows:

- Mid August 2025
 - o CC2 documentation to be finalised for PCA Review
- Late August 2025
 - o Anticipated approval of CC2.
- September 2025 – November 2025
 - o Commencement of superstructure works to Ground Floor, including detail excavation of pile caps, in ground drainage, precast columns and walls, FRP slab on ground.
- October 2025 – June 2026
 - o Duration of superstructure works from Level 1 to roof overrun including, FRP slabs, PT duct install, structural steel above L9 plantroom, post tensioning and back propping removal.

Refer to Figure 4a and 4b below for the overview of works under CC2.

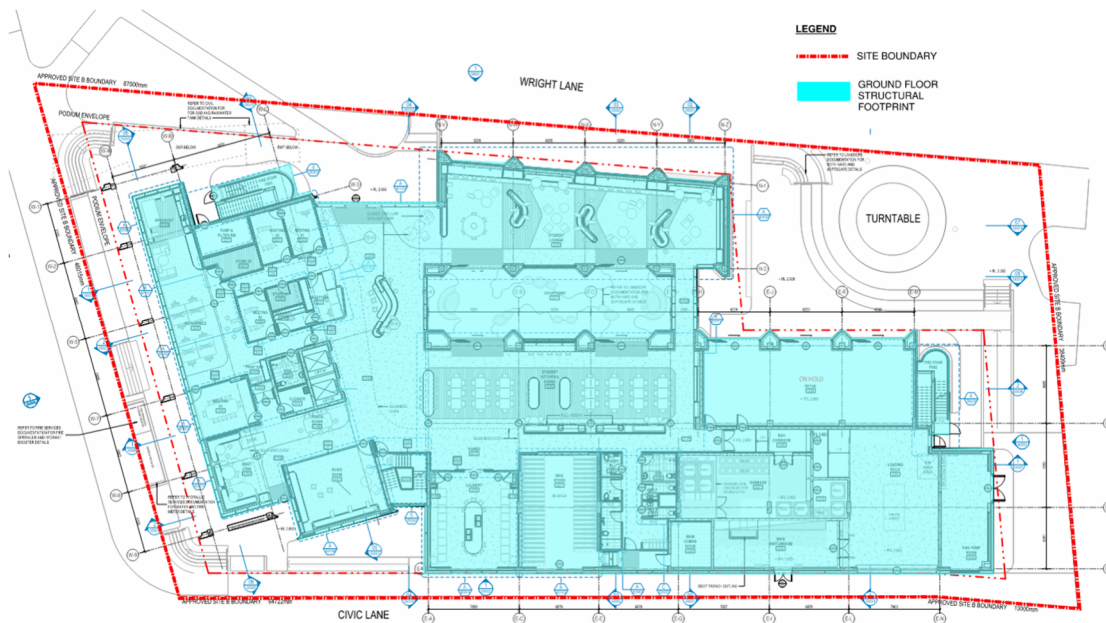


Figure 4a: Ground Plan Structural Overview

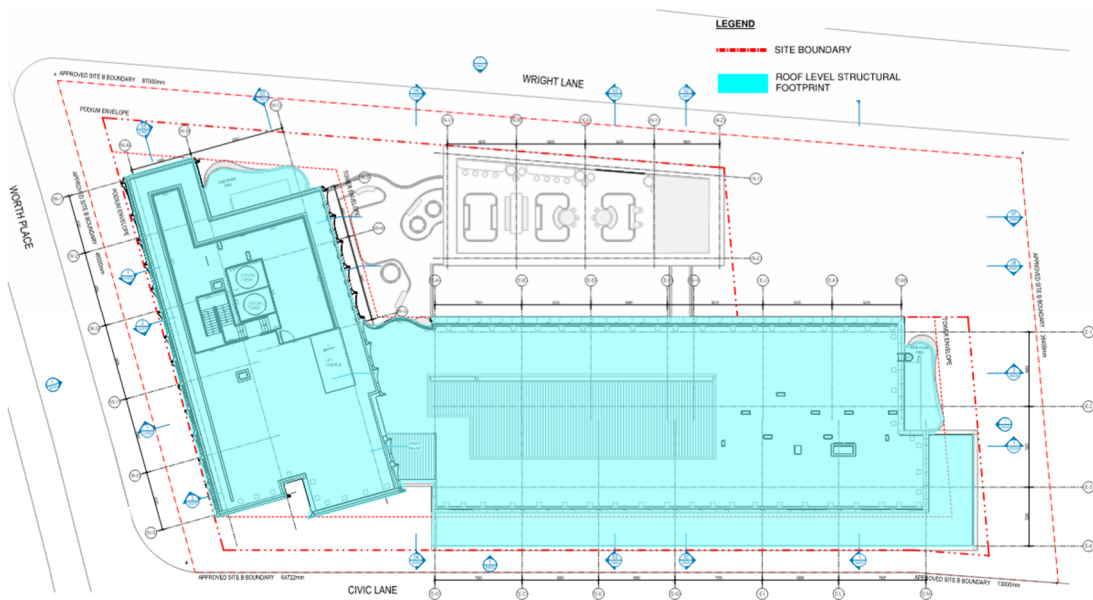


Figure 4b: Roof Plan Structural Overview

4.3 Construction Certificate 3 – Façade

The specific works included under this CC include:

- Façade works (including glazing, curtain wall and cladding)

The documentation for this CC will be prepared by Hansen Yuncken and the consultant design team and subcontractors. CC documentation for this phase will be collated in October 2025, with anticipated approval by late October 2025. All works under this CC will be completed from January 2026 – August 2026. The timeline for this CC is as follows:

- October 2025
 - o CC3 documentation to be finalised for PCA Review
- Late October 2025
 - o Anticipated approval of CC3.
- January 2026 – August 2026
 - o Duration of external cladding works including installation of curtain wall from ground level to Level 9, façade finishes, façade inspections, external signage and lighting.
- July 2026 – August 2026
 - o Balcony mesh installation, loading bay façade install, completion of plant room façade to stair O1 walls.

Refer to Figure 5 & 6 below for the overview of works under CC3.

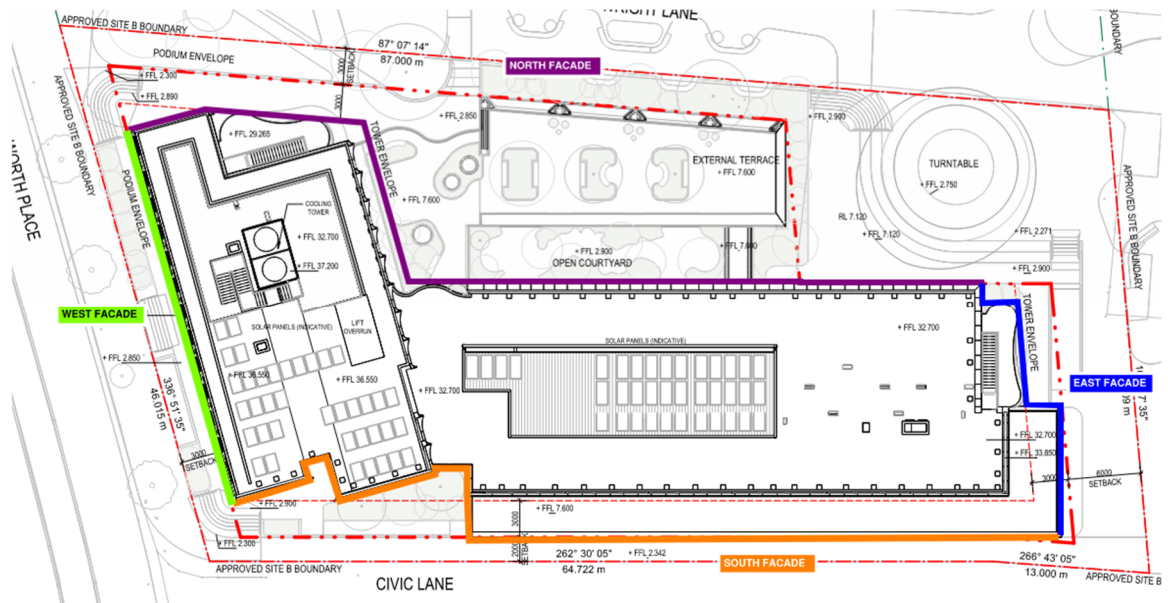


Figure 5: Overview of façade elevations (plan view)

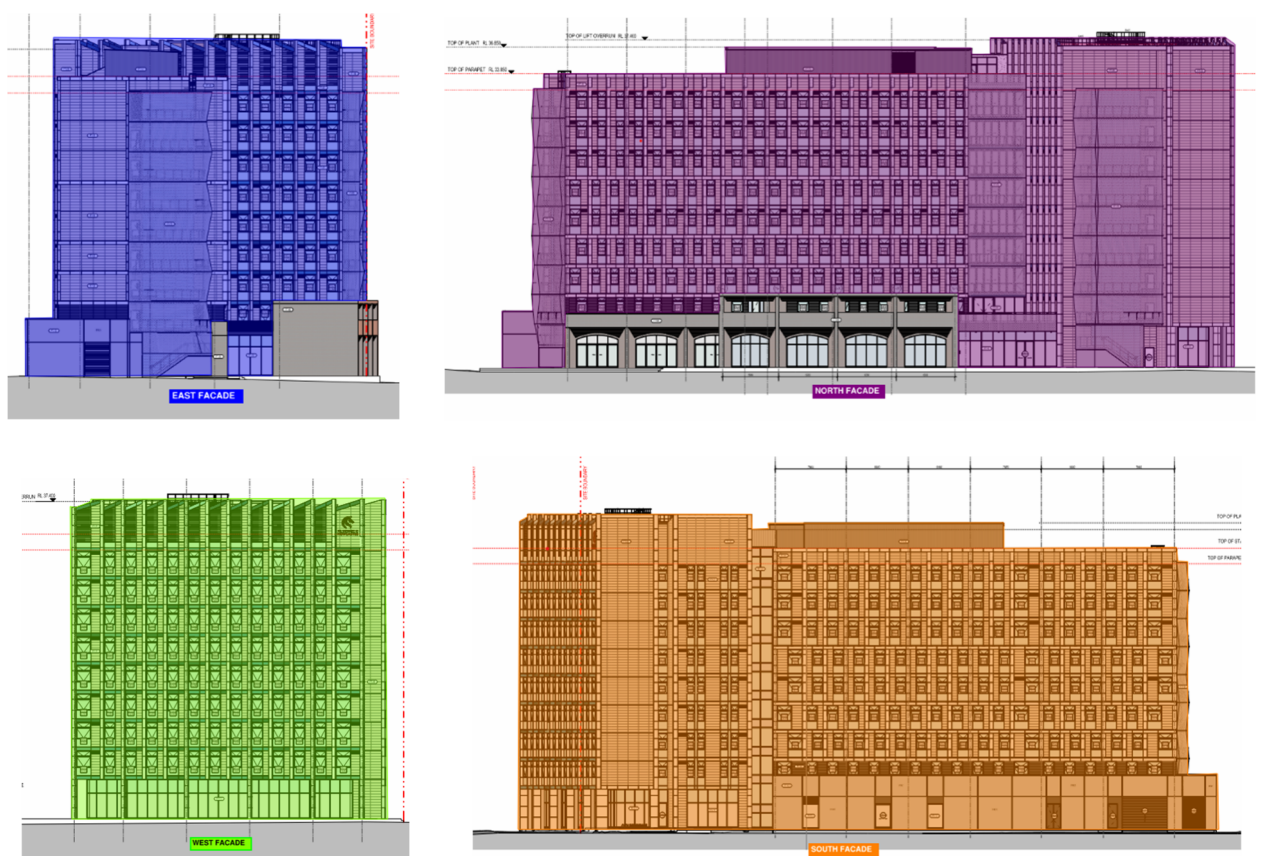


Figure 6: Overview of façade elevations (elevation view)

4.4 Construction Certificate 4 – Services and Finishes / Fitout

The specific works included under this CC include:

- Services works & commissioning
- Internal finishes and fitout

The documentation for this CC will be prepared by Hansen Yuncken and the consultant design team and subcontractors. The timeline for this CC is as follows:

- September 2025
 - o CC4 documentation to be finalised for PCA Review
- Late October 2025
 - o Anticipated approval of CC4.
- January 2026 – July 2026
 - o Ground floor, services rooms and retail internal works including: bathroom pod installation, high level services rough in, partitions and linings, joinery installation, wet area works, floor and wall finishes and services test and commissioning.
- February 2026 – September 2026
 - o Level 1 to Roof Plant internal works including: bathroom pod installation, high level services rough in, partitions and linings, joinery installation, wet area works, floor and wall finishes and services test and commissioning.

Refer to Figure 7 below for the overview of works under CC4.

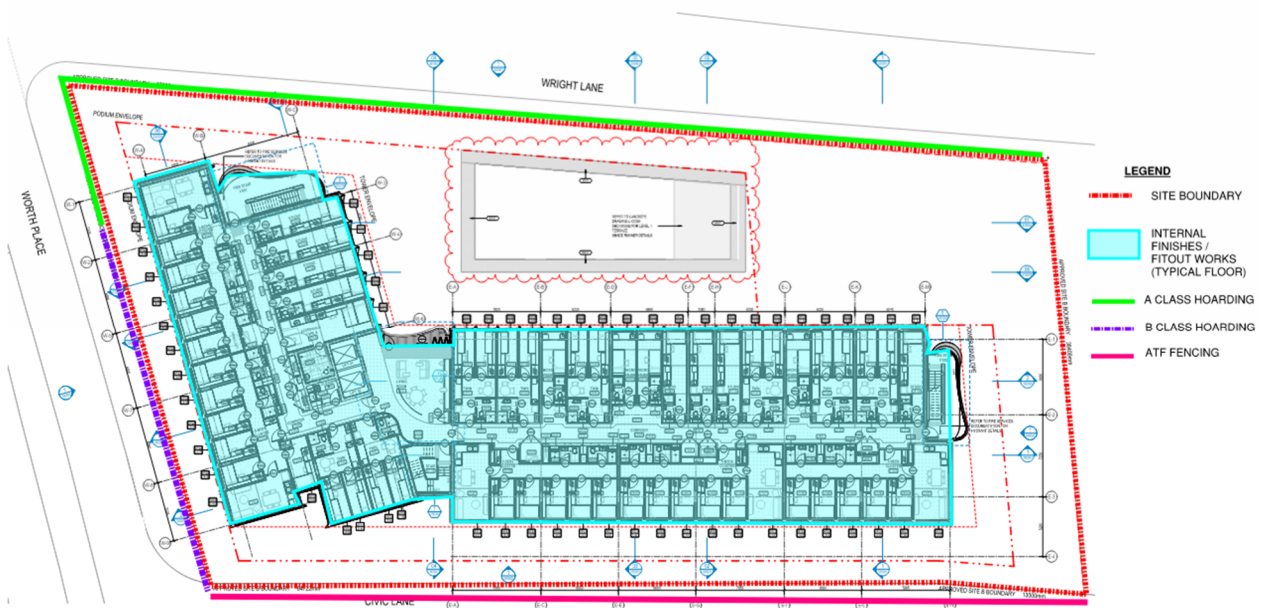


Figure 7: Overview of CC4 works.

4.5 Construction Certificate 5 – Balance of Works

The specific works included under this CC include:

- Landscaping works
- Lic domain works

The documentation for this CC will be prepared by Hansen Yuncken and the consultant design team and subcontractors. The timeline for this CC is as follows:

- November 2025
 - o CC5 documentation to be finalised for PCA Review
- Late November 2025
 - o Anticipated approval of CC5.
- April 2026 – July 2026
 - o Level 1 external terrace works including: construct planters and bench seating, drainage waterproof membranes, paving works, soft landscaping and install furniture and miscellaneous items.
- April 2026 – October 2026
 - o Building surround works including GF courtyard including: earthworks, soft landscaping works, paving works and installation of furniture and miscellaneous items.
- July 2026 – August 2026
 - o Public domain works including street landscaping, make good road and footpaths, external lighting and furniture works.

Refer to Figure 8, 9 & 10 below for the overview of works under CC5.



Figure 8: Ground Floor Zone 1 Public Domain and landscaping works

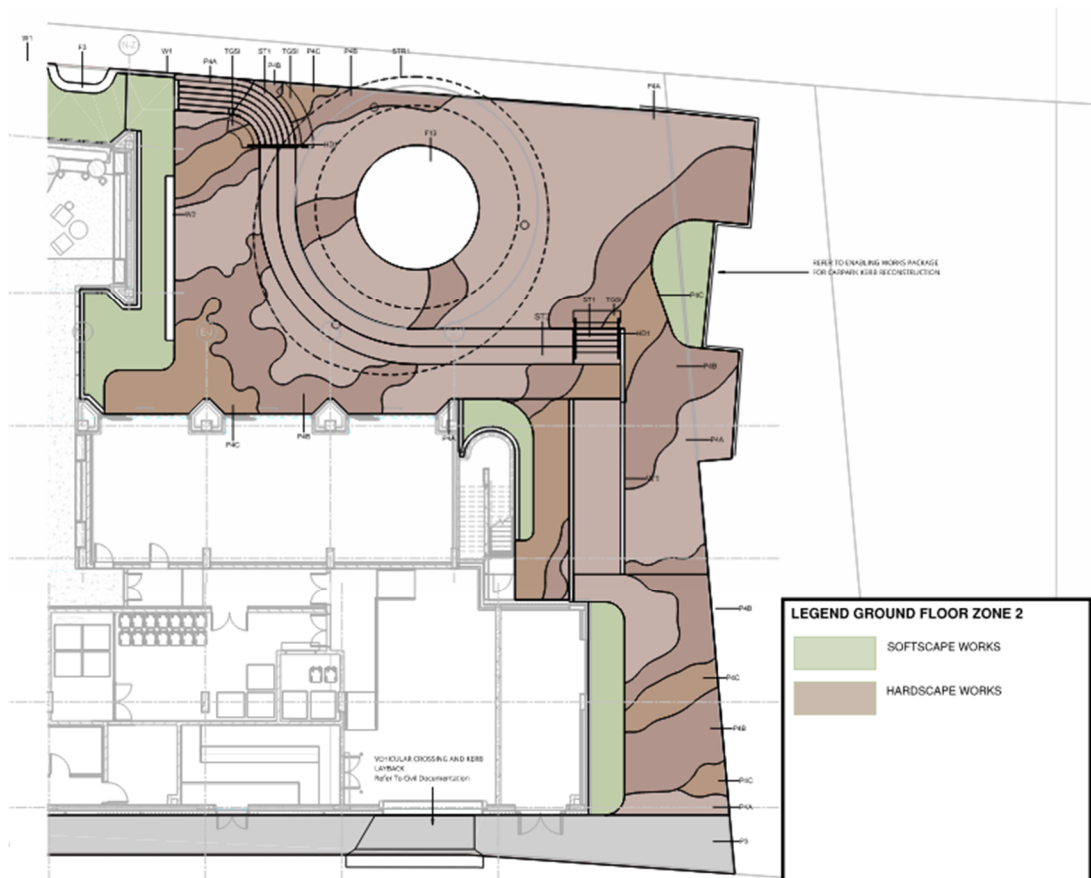


Figure 9: Ground Floor Zone 2 landscaping works.



Figure 10: Level 1 podium landscaping works

5 Operation

Following completion, the Applicant anticipates a single commencement of operation. As such a staged operation is not required.

6 Construction Risk Management

The Project proposes a staged Construction Certificate approach in order to de-risk and increase program efficiency. Common risks such as the design not being appropriately progressed, and authority approvals not being received in time for a single construction certificate are removed. The current approach allows flexibility, where an element of the work is not yet adequately designed or approved by an authority it can likely be shifted into a preceding Construction Certificate in order to maintain the program of works.

7 Conclusion

The University of Newcastle City Campus Student Accommodation Development will be constructed generally in-line with the abovementioned Construction Certificate staged approach over 5 separate CCs. All CCs will be prepared by the Head Contractor, Hansen Yuncken. There will be no staged occupation approach considered as part of the Staging Plan, and the project is expected to be completed and handed over to the Client by late-2026. The proposed stages will allow the works to be delivered in the most timely and efficient manner and minimise its impact on the community and ensure ample time is provided for the finalisation of the design prior to commencing each relevant stage of construction.

8 Appendices

8.1 SSDA Matrix

8.2 Construction Programme

8.1 SSDA Matrix

City Campus Student Accommodation SSDA Conditions of Consent Responsibility Matrix

CONDITION	DESCRIPTION	CC1 - In-ground Works	CC2 - Superstructure	CC3 - Façade	CC4 - Services and Finishes / Fitout	CC5 - Balance of Works	OC	Operation
	PART A ADMINISTRATIVE CONDITIONS							
A1	OBLIGATION TO MINIMISE HARM TO THE ENVIRONMENT In addition to meeting the specific performance measures and criteria in this consent, all reasonable and feasible measures must be implemented to prevent, and if prevention is not reasonable and feasible, minimise, any material harm to the environment that may result from the construction and operation of the development.	✓	✓	✓	✓	✓		
A2	TERMS OF CONSENT The development may only be carried out: (a) in compliance with the conditions of this consent; (b) in accordance with all written directions of the Planning Secretary; (c) in accordance with the EIS, the Applicant's Response to Submissions, and the Applicant's Response to Requests for Further Information; and (d) in accordance with the approved plans in the table below, as modified by the conditions of this consent: <i>(Note: for drawing table refer to SSDA consent)</i>	✓	✓	✓	✓	✓		
A3	Consistent with the requirements in this consent, the Planning Secretary may make written directions to the Applicant in relation to: (a) the content of any strategy, study, system, plan, program, review, audit, notification, report or correspondence submitted under or otherwise made in relation to this consent, including those that are required to be, and have been, approved by the Planning Secretary; and (b) the implementation of any actions or measures contained in any such document referred to in condition A3(a) above. (c) the implementation of any actions or measures contained in any such document referred to in (a) above.	As required	As required	As required	As required	As required		
A4	The conditions of this consent and directions of the Planning Secretary prevail to the extent of any inconsistency, ambiguity or conflict between them and a document listed in condition A2(c). In the event of an inconsistency, ambiguity or conflict between any of the documents listed in conditions A2(c), the most recent document prevails to the extent of the inconsistency, ambiguity or conflict.	✓	✓	✓	✓	✓		
A5	LIMITS ON CONSENT This consent will lapse five years from the date of the consent unless the works associated with the development have physically commenced.	✓						
A6	PRESCRIBED CONDITIONS The Applicant must comply with all relevant prescribed conditions of development consent under Part 6, Division 8A of the EP&A Regulation	✓	✓	✓	✓	✓		
A7	PLANNING SECRETARY AS MODERATOR In the event of a dispute between the Applicant and a public authority, in relation to an applicable requirement in this approval or relevant matter relating to the development, either party may refer the matter to the Planning Secretary for resolution. The Planning Secretary's resolution of the matter must be binding on the parties.	As required	As required	As required	As required	As required		
A8	LEGAL NOTICES Any advice or notice to the consent authority must be served on the Planning Secretary.	As required	As required	As required	As required	As required		
A9	REVISION OF STRATEGIES, PLANS AND PROGRAMS Within three months of: (a) the submission of a compliance report under condition B11 - B13; (b) the submission of an incident report under condition A13; (c) the approval of any modification of the conditions of this consent; or (d) the issue of a direction of the Planning Secretary under condition A3 which requires a review, the strategies, plans and programs required under this consent must be reviewed, and the Department must be notified in writing that a review is being carried out.	✓	✓	✓	✓	✓		
A10	If necessary to either improve the environmental performance of the development, cater for a modification or comply with a direction, the strategies, plans and programs required under this consent must be revised, to the satisfaction of the Planning Secretary. Where revisions are required, the revised document must be submitted to the Planning Secretary for approval within six weeks of the review. <i>Note: This is to ensure strategies, plans and programs are updated on a regular basis and to incorporate any recommended measures to improve the environmental performance of the development.</i>	✓	✓	✓	✓	✓		
A11	EVIDENCE OF CONSULTATION Where conditions of this consent require consultation with an identified party, the Applicant must: (a) consult with the relevant party prior to submitting the subject document to the Planning Secretary or Certifier for information or approval; and (b) provide details of the consultation undertaken including: (i) the outcome of that consultation, matters resolved and unresolved; and (ii) details of any disagreement remaining between the party consulted and the Applicant and how the Applicant has addressed the matters not resolved.	As required	As required	As required	As required	As required		
A12	STRUCTURAL ADEQUACY All new buildings and structures, and any alterations or additions to existing buildings and structures, that are part of the development, must be constructed in accordance with: (a) the relevant requirements of the NCC; (b) any additional requirements of the Subsidence Advisory NSW where the building or structure is located on land within a declared Mine Subsidence District. <i>Note 1: Part 8 of the EP&A Regulation sets out the requirements for the certification of the development</i>	✓	✓	✓	✓	✓		
A13	INCIDENT NOTIFICATION, REPORTING AND RESPONSE The Department must be notified via the Major projects website immediately after the Applicant becomes aware of an incident. The notification must identify the development (including the development application number and the name of the development if it has one) and set out the location and nature of the incident. Subsequent notification must be given and reports submitted in accordance with the requirements set out in Appendix 1.	As required	As required	As required	As required	As required		
A14	NON-COMPLIANCE NOTIFICATION Within seven days of becoming aware of a non-compliance, the Applicant must notify the Department of the non-compliance. The notification must be in writing and must be submitted via the NSW planning portal (Major Projects).	As required	As required	As required	As required	As required		
A15	The notification must identify the development (including the development application number and name), set out the condition of this consent that the development is non-compliant with, why it does not comply, the reasons for the non-compliance (if known), and what actions have been undertaken, or will be undertaken, and when, to address the non-compliance.	As required	As required	As required	As required	As required		
A16	A non-compliance which has been notified as an incident does not need to also be notified as a non-compliance	As required	As required	As required	As required	As required		
A17	MONITORING AND ENVIRONMENTAL AUDITS Any condition of this consent that requires the carrying out of monitoring or an environmental audit, whether directly or by way of a plan, strategy or program, is taken to be a condition requiring monitoring or an environmental audit under Division 9.4 of Part 9 of the EP&A Act. This includes conditions in respect of incident notification, reporting and response, non-compliance notification and independent environmental auditing. <i>Note 1: For the purposes of this condition, as set out in the EP&A Act, "monitoring" is monitoring of the development to provide data on compliance with the consent or on the environmental impact of the development, and an "environmental audit" is a periodic or particular documented evaluation of the development to provide information on compliance with the consent or the environmental management or impact of the development.</i>	✓	✓	✓	✓	✓		
A18	APPLICABILITY OF GUIDELINES References in the conditions of this consent to any guideline, protocol, Australian Standard or policy are to such guidelines, protocols, Standards or policies in the form they are in as at the date of this consent.	✓	✓	✓	✓	✓		
A19	Consistent with the conditions of this consent and without altering any limits or criteria in this consent, the Planning Secretary may, when issuing directions under this consent in respect of ongoing monitoring and management obligations, require compliance with an updated or revised version of such a guideline, protocol, Standard or policy, or a replacement of them.	As required	As required	As required	As required	As required		
A20	STAGING The project may be constructed and operated in stages. Where compliance with conditions is required to be staged due to staged construction or operation, a Staging Report (for either or both construction and operation as the case may be) must be prepared and submitted to the satisfaction of the Planning Secretary. The Staging Report must be submitted to the Planning Secretary no later than one month before the commencement of construction of the first of the proposed stages of construction (or if only staged operation is proposed, one month before the commencement of operation of the first of the proposed stages of operation).	✓	Update if required	Update if required	Update if required	Update if required		
A21	EXTERNAL MATERIALS The external colours, materials and finishes of the buildings must be consistent with the approved plans referenced in condition A2. Any minor changes to the colour and finish of approved external materials may be approved by the Certifier, provided that: (a) the alternative colour/material is of a similar tone/shade and finish to the approved, external colours/building materials; (b) the quality and durability of any alternative material is the same standard as the approved, external building materials; and (c) a copy of any approved changes to the external colours and/or building materials is provided to the Planning Secretary for information.			✓	✓	✓		
A22	COMPLIANCE The Applicant must ensure that all of its employees, contractors (and their sub-contractors) are made aware of, and are instructed to comply with, the conditions of this consent relevant to activities they carry out in respect of the development.	✓	✓	✓	✓	✓		
A23	HOUSING AND PRODUCTIVITY CONTRIBUTIONS Prior to the commencement of works, the Housing and Productivity Contribution (HPC) set out in the table below is required to be made: Housing and Productivity Contribution Amount Total housing and productivity contribution \$3,900.00 <i>Note: The contribution amount is subject to indexation in accordance with the Environmental Planning and Assessment (Housing and Productivity Contributions) Order 2024 at the time of payment. A request for assessment of the adjusted amount and instructions on how to make a payment can be made by contacting hpc.enquiry@planning.nsw.gov.au.</i>	✓						
	PART B PRIOR TO COMMENCEMENT OF WORKS							
B1	DESIGN AMENDMENTS AMENDMENTS Prior to commencement of the Civic Lane works under this consent, the Applicant must submit for approval by the Planning Secretary: (a) an amended Public Domain Works Plan as referenced in condition A2 to reflect the Public Domain Works Plan – CN Mark-Up prepared by Council dated 15/04/2025; (b) revised plans demonstrating that the doors of the Main Comms Room and Main Switchroom have been redesigned so as to not open outwards across the proposed shared path.					✓		
B2	NOTIFICATIONS AND COMMENCEMENT OF WORKS NOTIFICATION OF COMMENCEMENT The Department must be notified to the Department in writing of the dates of commencement of physical work and operation at least 48 hours before those dates.	✓						
B3	If the construction of the development is to be staged, the Department must be notified in writing at least 48 hours before the commencement of each stage, of the date of commencement and the development to be carried out in that stage.		✓	✓	✓	✓		
B4	UTILITY SERVICES Prior to the commencement of work, the Applicant is to negotiate with the utility authorities (e.g. Ausgrid and Telecommunications Carriers) in connection with the relocation and/or adjustment of the services affected by the construction of the underground structure.	✓						
B5	Prior to the commencement of work, other than above ground demolition and site clearing works, written advice must be obtained from the electricity supply authority, an approved telecommunications carrier and an approved gas carrier (where relevant) stating that satisfactory arrangements have been made to ensure provision of adequate services.	✓						
B6	DIAL BEFORE YOU DIG Prior to the commencement of any excavation on or near the site, the Applicant must submit to the Certifier written confirmation from NSW Dial Before You Dig Service that the proposed excavation will not conflict with any underground utility services.	✓						
B7	CERTIFIED PLANS Plans certified in accordance with section 6.16 of the EP&A Act are to be submitted to the Certifier and the Department prior to commencement of each stage of the works and shall include details as required by any of the following conditions.	✓	✓	✓	✓	✓		
B8	ACCESS TO INFORMATION At least 48 hours before the commencement of construction until the completion of all works under this consent, or such other time as agreed by the Planning Secretary, the Applicant must: (a) make the following information and documents (as they are obtained or approved) publicly available on its website: (i) the documents referred to in condition A2 of this consent; (ii) all current statutory approvals for the development; (iii) all approved strategies, plans and programs required under the conditions of this consent; (iv) regular reporting on the environmental performance of the development in accordance with the reporting arrangements in any plans or programs approved under the conditions of this consent; (v) a comprehensive summary of the monitoring results of the development, reported in accordance with the specifications in any conditions of this consent, or any approved plans and programs; (vi) a summary of the current stage and progress of the development; (vii) contact details to enquire about the development or to make a complaint; (viii) a complaints register, updated monthly; (ix) audit reports prepared as part of any independent environmental audit of the development and the Applicant's response to the recommendations in any audit report; (x) any other matter required by the Planning Secretary; and (b) keep such information up to date to the satisfaction of the Planning Secretary.	✓	Maintain and update as required	Maintain and update as required	Maintain and update as required	Maintain and update as required		
B9	COMMUNITY COMMUNICATION STRATEGY A community Communication Strategy must be prepared to provide mechanisms to facilitate communication between the Applicant, Council and the community (including adjoining affected landowners and businesses, and others directly impacted by the development), during the design and construction of the development and for a minimum of 12 months following the completion of construction.	✓	Maintain and update as required	Maintain and update as required	Maintain and update as required	Maintain and update as required		
B10	The Community Communication Strategy must: (a) identify people to be consulted during the design and construction phases; (b) set out procedures and mechanisms for the regular distribution of accessible information about or relevant to the development; (c) provide for the formation of community-based forums, if required, that focus on key environmental management issues for the development; (d) set out procedures and mechanisms: (i) through which the community can discuss or provide feedback to the Applicant; (ii) through which the Applicant will respond to enquiries or feedback from the community; and (iii) to resolve any issues and mediate any disputes that may arise in relation to construction and operation of the development, including disputes regarding rectification or compensation. The Community Communications Strategy must be submitted to the Planning Secretary no later than one month before the commencement of any work and must be implemented for a minimum of 12 months following the completion of construction.	✓	Maintain and update as required	Maintain and update as required	Maintain and update as required	Maintain and update as required		
B11	COMPLAINTS AND ENQUIRIES PROCEDURE Prior to the commencement of construction works the following must be made available for community enquiries and complaints for the duration of construction: (a) a 24-hour telephone number(s) on which complaints and enquiries about the carrying out of any works may be registered; (b) a postal address to which written complaints and enquiries may be sent; and (c) an email address to which electronic complaints and enquiries may be transmitted.	✓	Maintain and update as required	Maintain and update as required	Maintain and update as required	Maintain and update as required		

City Campus Student Accommodation								
SSDA Conditions of Consent Responsibility Matrix								
CONDITION	DESCRIPTION	CC1 - Inground Works	CC2 - Superstructure	CC3 - Façade	CC4 - Services and Finishes / Fitout	CC5 - Balance of Works	OC	Operation
B12	PUBLIC LIABILITY INSURANCE Prior to the commencement of any works on or below Council land, the Applicant must submit to the satisfaction of the Certifier evidence of Public Liability Insurance, with a minimum liability of \$20 million. A copy of the Insurance cover is to be provided to Council.	✓	Maintain throughout works	Maintain throughout works	Maintain throughout works	Maintain throughout works		
B13	CROWN BUILDING WORK Crown building work cannot be commenced unless the relevant Crown Building work is certified by or on behalf of the Crown to comply with the technical provisions of the State's building laws in force as at: (a) the date of the invitation for tenders to carry out Crown building work; or (b) in the absence of tenders, the date on which the Crown building work commences.	✓	✓	✓	✓	✓		
B14	PRE-CONSTRUCTION REQUIREMENTS ECOLOGICALLY SUSTAINABLE DEVELOPMENT (ESD) Prior to the commencement of construction, the Applicant must register for a Green Star Buildings v1 rating with the Green Building Council Australia and submit evidence of registration to the Certifier.	✓						
B15	EXTERNAL WALLS AND CLADDING The external walls and cladding must comply with the relevant requirements of the NCC.			✓				
B16	Prior to the commencement of construction of external walls and cladding, the Applicant must provide the Certifier with documented evidence that the products and systems proposed for use or used in the construction of external walls including finishes and claddings such as synthetic or aluminium composite panels comply with the requirements of the NCC.			✓				
B17	NATIONAL CONSTRUCTION CODE COMPLIANCE The proposed works must comply with the applicable performance requirements of the NCC to achieve and maintain acceptable standards of structural sufficiency, safety (including fire safety), health and amenity for the ongoing benefit of the community. Compliance with the performance requirements can only be achieved by: (a) complying with the deemed to satisfy provisions; or (b) formulating an alternative solution which: (i) complies with the performance requirements; or (ii) is shown to be at least equivalent to the deemed to satisfy provision; or (iii) a combination of (a) and (b).	✓	✓	✓	✓	✓		
B18	MAXIMUM HEIGHT The maximum height of the approved building must not exceed RL 37.53m AHD, including plant and lift overruns, communication devices, antennae, satellite dishes, masts, flagpoles, chimneys, flues and the like. Details confirming compliance must be submitted to the Certifier prior to the commencement of above ground works.		✓					
B19	COMPLIANCE WITH ACOUSTIC ASSESSMENT Prior to the commencement of above ground works, the Applicant must submit a Report to the Certifier from an acoustic Engineer demonstrating that the design of the development has incorporated all performance parameters, requirements, engineering assumptions and recommendations contained in the Noise and Vibration Assessment, prepared by ACOR Consultants and dated 17 June 2024.		✓					
B20	COMPLIANCE WITH WIND IMPACT ASSESSMENT Prior to the commencement of above ground works, the Applicant must submit a Report to the Certifier demonstrating that the design of the development has incorporated the wind mitigation measures contained within the document titled Pedestrian Wind Environment Assessment, prepared by Windtech Consultants dated 15 July 2024.		✓					
B21	STORMWATER QUALITY ASSESSMENT The development must comply with the Integrated Water Management Report (Flooding and Stormwater) prepared by TTW PTY LTD dated 8 August 2024. Prior to commencement of substructure works, a design certification report prepared by a suitably qualified practitioner engineer demonstrating compliance with approved MUSIC link targets and parameters must be submitted to the Certifier. The report must include a response to all stormwater quality improvement devices structural integrity, treatment train and their treatment properties demonstrating compliance with the approved MUSIC link reports.		✓					
B22	FLOOD PLANNING LEVELS The development must be constructed to comply with the recommended flood planning levels indicated in the Flood Impact Risk Assessment, Revision 04, prepared by Torrent Consulting dated 03 March 2025.	✓	✓					
B23	OUTDOOR LIGHTING All outdoor lighting within the site shall comply with, where relevant, AS/NZ1158.3: 1999 Pedestrian Area (Category P) Lighting and AS4282: 1997 Control of the Obtrusive Effects of Outdoor Lighting. Details demonstrating compliance with these requirements are to be submitted to the Certifier prior to the commencement of public domain works.					✓		
B24	STRUCTURAL DETAILS Prior to the commencement of substructure works, the Applicant must submit to the Certifier, the relevant structural drawings prepared and signed by a suitably qualified practising Structural Engineer that demonstrates compliance with: (a) the relevant clauses of the NCC; and (b) the development consent.	✓						
B25	Prior to the commencement of all works not subject to condition B27, the Applicant must submit to the Certifier, the relevant structural drawings prepared and signed by a suitably qualified practising Structural Engineer that demonstrates compliance with: (a) the relevant clauses of the NCC; and (b) the development consent.		✓					
B26	REFLECTIVITY The building materials must have a maximum normal specular reflectivity of visible light of 20 per cent. If the proposed building materials do not comply with the above reflectivity requirement, then an alternate materials / mitigation measures must be proposed so that the facades of the building would not result in glare that causes any discomfort or threatens the safety of pedestrians or drivers.			✓				
B27	A statement prepared by a suitably qualified expert, demonstrating compliance with the requirements of condition B29 must be submitted to the satisfaction of the Certifier prior to the commencement of the cladding of the external facades.			✓				
B28	MECHANICAL PLANT NOISE MITIGATION Details of noise mitigation measures for all mechanical plant are to be detailed on the relevant Construction drawings. Certification from an appropriately qualified acoustic engineer that the proposed measures will achieve compliance with the requirements of the NSW Industrial Noise Policy is required to be submitted to the Certifier prior to the commencement of above ground works.		✓					
B29	MECHANICAL VENTILATION All mechanical ventilation systems shall be installed in accordance with the NCC and shall comply with Australian Standards AS1668.2 and AS3666 - Microbial Control of Air Handling and Water Systems of Building, to ensure adequate levels of health and amenity to the occupants of the building and to ensure environment protection. Details shall be submitted to the Certifier prior to the commencement of above ground works.		✓					
B30	The mechanical exhaust system for the ground floor retail tenancy is to be designed to be capable of accommodating exhaust requirements in accordance with relevant Australia Standards, in order to allow for the event that the tenancy is approved for future use as a food premises or other use which requires mechanical exhaust.				✓			
B31	SANITARY FACILITIES FOR DISABLED PERSONS The Applicant shall ensure that the provision of sanitary facilities for disabled persons complies with Section F2.4 of the NCC.				✓			
B32	ACCESS FOR PEOPLE WITH DISABILITIES Access and facilities for people with disabilities must be designed in accordance with the NCC. Prior to the commencement of above ground works, the Certifier must ensure that evidence of compliance with this condition from an appropriately qualified person is provided and that the requirements are referenced on any certified plans. Applicant must submit to the satisfaction of the Certifier		✓					
B33	CRIME PREVENTION THROUGH ENVIRONMENTAL DESIGN (CPTED) To minimise the opportunity for crime, the recommendations of the CPTED Report prepared by Ethos Urban dated 22 November 2024 and the revised Preliminary Operational Management Plan prepared by the University of Newcastle, dated 14 March 2025 are to be revised by a suitability qualified expert to incorporate CPTED treatments that specifically respond to the suburb's mid-to high rated crime hotspot offence categories, including stealing from motor vehicles and dwelling, and assaults (non-domestic). Details demonstrating compliance with the requirements are to be submitted to the Certifier prior to the commencement of above ground works.		✓					
B34	TACTILE GROUND SURFACE INDICATORS AND HANDRAILS All tactile ground surface indicators, handrails and other elements required to provide access into the building/property must be located entirely within the private property boundary.					✓		
B35	COMPLIANCE WITH ACOUSTIC REPORT PORT RELATED – PORT AUTHORITY Prior to the commencement of above ground works, verification shall be provided to the consent authority that the development has been designed and will be constructed to achieve the Design Noise Levels noted in the EIS and Acoustic Assessment, with regards to including port-related noise.		✓					
B36	ADAPTABLE UNITS Prior to the commencement of above ground works, the Applicant must submit to the Certifier a Report demonstrating that any adaptable units specified in the approved plans or supporting documentation comply with the applicable Australian Standards.		✓					
B37	MANAGEMENT PLANS CONSTRUCTION ENVIRONMENTAL MANAGEMENT PLAN Prior to the commencement of any works, a Construction Environmental Management Plan (CEMP) shall be submitted to the Certifier. The CEMP must address, but not be limited to, the following matters where relevant: (a) Details of: (i) hours of work (ii) 24 hour contact details of the site manager (iii) community consultation and complaint handling procedure (iv) traffic management (v) noise and vibration management, prepared by a suitably qualified person (vi) management of dust and odour to protect the amenity of the neighbourhood (vii) stormwater control and discharge, including measures to ensure that sediment and other materials are not tracked onto the roadway by vehicles leaving the site (viii) prevention and contamination management, including any unexpected contamination finds protocol (ix) waste management (x) external lighting in compliance with applicable Australian Standards (xi) site security, including fencing or hoarding (xii) flora and fauna management. (b) Construction Pedestrian and Traffic Management Sub-Plan in accordance with condition B41; (c) Construction Noise and Vibration Management Sub-Plan in accordance with condition B42; (d) Construction Waste Management Sub-Plan in accordance with condition B43; (e) Construction Soil and Water Management Sub-Plan in accordance with condition B44; (f) an unexpected finds protocol for contamination and associated communications procedure in accordance with condition B54; (g) an unexpected finds protocol for Aboriginal and non-Aboriginal heritage and associated communications procedure in accordance with conditions B55 and B59; and (h) waste classification (for materials to be removed) and validation (for materials to remain) to be undertaken to confirm the contamination status in these areas of the site.	✓	Maintain and update as required	Maintain and update as required	Maintain and update as required	Maintain and update as required		
B38	CONSTRUCTION PEDESTRIAN AND TRAFFIC MANAGEMENT SUB-PLAN Prior to the commencement of any works, the Applicant must submit to the Certifier a final Construction Pedestrian and Traffic Management Plan Sub-Plan (CPTMP) for the development with measures to reduce environmental impacts and harm during construction of the development arising from construction traffic, including, at a minimum, the following information: (a) location of any proposed work zone(s); (b) construction vehicle access arrangements and haulage routes; (c) predicted number and timing of construction vehicle movements and vehicle types; (d) identification of potential conflicts between vehicle movements required for construction and general traffic, cyclists, pedestrians, bus services within the vicinity of the site from construction vehicles; (e) be prepared in consultation with Council; and (f) Settlement Lane must not be used by heavy construction vehicles because of weight load restrictions.	✓	Maintain and update as required	Maintain and update as required	Maintain and update as required	Maintain and update as required		
B39	CONSTRUCTION NOISE AND VIBRATION MANAGEMENT SUB-PLAN Prior to the commencement of any works, the Applicant must submit to the Certifier a Construction Noise and Vibration Management Sub Plan (CNVMP) for the development, prepared by a suitably qualified person, with measures to minimise environmental impacts and harm during construction of the development arising from construction noise and vibration, including, at a minimum, the following: (a) identification of noise sources and sensitive receivers. (b) quantification of the rating background noise level (RBL) for sensitive receivers; (c) describe procedures for achieving the noise management levels in EPA's Interim Construction Noise Guideline (DECC, 2009) (ICNG) (as may be updated or replaced from time to time) (d) prediction and assessment of potential noise, ground-borne noise (as relevant) and vibration levels from the proposed construction methods expected at Sensitive Receiver premises against the objectives identified in the ICNG (e) noise mitigation measures that can be implemented to reduce construction noise and vibration impacts, including: (i) installation of acoustic barriers/enclosures; and (ii) alternative excavation methods; (f) describe the measures to be implemented to manage high noise generating works such as piling, in close proximity to sensitive receivers; (g) measures to identify non-conformances with the requirements of the CNVMP, and procedures to implement corrective and preventative action and to respond to complaints; (h) procedures for notifying residents of construction activities that are likely to affect their noise and vibration amenity; and (i) include a complaints management system that would be implemented for the duration of the development	✓	Maintain and update as required	Maintain and update as required	Maintain and update as required	Maintain and update as required		
B40	CONSTRUCTION WASTE MANAGEMENT SUB-PLAN Prior to the commencement of any works, the Applicant must submit to the Certifier a Construction Waste Management Sub Plan (CWMP) for the development. The CWMP must include, as a minimum, the following information: (a) requirement that all waste generated during the project is assessed, classified and managed in accordance with the EPA's "Waste Classification Guidelines Part 1: Classifying Waste"; (b) demonstrate that an appropriate area will be provided for the storage of garbage bins and recycling containers and all waste and recyclable material generated by the works; (c) procedures for minimising the movement of waste material around the site and double handling; (d) requirement that waste (including litter, debris or other matter) is not caused or permitted to enter any waterways; (e) requirement that any vehicle used to transport waste or excavation spoil from the site is covered before leaving the premises; (f) requirement that the wheels of any vehicle, trailer or mobilised plant leaving the site are cleaned of debris prior to leaving the premises; and (g) details in relation to the transport of waste material within the site and from the site, including (at a minimum): (i) a traffic plan showing transport routes within the site; (ii) a commitment to retain waste transport details for the life of the project to demonstrate compliance with the Protection of the Environment Operations Act 1997; and (iii) the name and address of each licensed facility that will receive waste from the site.	✓	Maintain and update as required	Maintain and update as required	Maintain and update as required	Maintain and update as required		

City Campus Student Accommodation								
SSDA Conditions of Consent Responsibility Matrix								
CONDITION	DESCRIPTION	CC1 - In-ground Works	CC2 - Superstructure	CC3 - Façade	CC4 - Services and Finishes / Fitout	CC5 - Balance of Works	OC	Operation
B41	CONSTRUCTION SOIL AND WATER MANAGEMENT PLAN SUB-PLAN Prior to the commencement of any works, the Applicant must submit to the Certifier a Construction Soil and Water Management Sub-Plan (CSWMP) for the development. The CSWMP must be prepared by a suitably qualified expert, in Consultation with Council and include, at a minimum, the following information: (a) describe all erosion and sediment controls to be implemented during construction (b) details of measures to be implemented to ensure that sediment and other materials are not tracked onto the roadway by vehicles leaving the site. (c) provide a plan of how all construction works will be managed in a wet-weather event (i.e. storage of equipment, stabilisation of the site); (d) detail all off-site flows from the site during construction; and (e) describe the measures that must be implemented to manage stormwater and flood flows for small and large sized events, including, but not limited to 1 in 1-year ARI, 1 in 5-year ARI and 1 in 100-year ARI.	✓	Maintain and update as required	Maintain and update as required	Maintain and update as required	Maintain and update as required		
B42	FLOOD MANAGEMENT Prior to the commencement of any earthwork or construction, the Applicant must prepare and implement for the duration of the works: (a) flood warning and notification procedures for construction workers on the site; and (b) evacuation and refuge protocols.	✓	Maintain and update as required	Maintain and update as required	Maintain and update as required	Maintain and update as required		
B43	GEOTECHNICAL DESIGN, CERTIFICATION AND MONITORING PLAN Prior to the commencement of any works, the applicant must engage a suitably qualified and practicing Engineer having experience in the geotechnical and hydrogeological fields, to design, certify and oversee the construction of all subsurface structures associated with the development. This engineer is to prepare the following documentation: (a) Certification that the civil and structural details of all subsurface structures are designed to: (i) provide appropriate support and retention to neighbouring property; (ii) ensure there will be no ground settlement or movement during excavation or after construction (whether by the act of excavation or dewatering of the excavation) sufficient to cause an adverse impact to adjoining property or public infrastructure; and (iii) ensure that the treatment and drainage of groundwater will be undertaken in a manner which maintains the pre-developed groundwater regime, so as to avoid constant or ongoing seepage to the public drainage network and structural impacts that may arise from alteration of the pre-developed groundwater table. (b) A Geotechnical Monitoring Plan (GMP) to be implemented during construction that: (i) is based on a geotechnical investigation of the site and subsurface conditions, including groundwater; (ii) details the location and type of monitoring systems to be utilised, including those that will detect the deflection of all shoring structures, settlement and excavation induced ground vibrations to the relevant Australian Standard; (iii) details recommended hold points and trigger levels of any monitoring systems, to allow for the inspection and certification of geotechnical and hydro-geological measures by the professional engineer; and (iv) details an action plan and contingency for the principal building contractor in the event these trigger levels are exceeded.	✓	Maintain and update as required	Maintain and update as required	Maintain and update as required	Maintain and update as required		
B44	The certification and the GMP is to be submitted to the Certifier prior to the commencement of any works other than any above ground demolition and site clearing works. Copies of the certification and GMP must be provided to the Planning Secretary.	✓						
B45	PRE-CONSTRUCTION DOCUMENTATION AND MEASURES PRE-CONSTRUCTION DILAPIDATION REPORT The Applicant is to engage a qualified structural engineer to prepare a Pre-Construction Dilapidation Report detailing the current structural condition of all retained existing and adjoining buildings, infrastructure and roads within the 'zone of influence'. The report shall be submitted to the Certifier prior to any works commencing. A copy of the report must be forwarded to the Council and each of the affected property owners. The Pre-Construction Dilapidation Report shall also include a photographic recording of the public domain site frontages and must be submitted to Council. The recording must include clear images of the footpath, nature strip, kerb and gutter, driveway crossovers and laybacks, kerb ramps, road carriageway, street trees and plantings, parking restriction and traffic signs, and all other existing infrastructure along the street. The form of the recording is to be as follows: (a) a PDF format report containing all images at a scale that clearly demonstrates the existing site conditions; (b) each image is to be labelled to identify the elements depicted, the direction that the image is viewed towards, and include the name of the relevant street frontage; (c) each image is to be numbered and cross referenced to a site location plan; (d) a summary report, prepared by a suitable qualified professional, must be submitted in conjunction with the images detailing the project description, identifying any apparent existing defects, detailing the date and authorship of the photographic record, the method of documentation and limitations of the photographic record; and (e) include written confirmation, issued with the authority of both the Applicant and the photographer that Council is granted a perpetual non-exclusive license to make use of the copyright in all images supplied, including the right to make copies available to third parties as though they were Council images. The signatures of both the applicant and the photographer must be included.	✓						
B46	SURVEY CERTIFICATE Prior to the commencement of above ground works, the Applicant must cause the building to be set out by a Registered Surveyor to verify the correct position of all structures in relation to site boundaries and the approved alignment levels, and cause the Registered Surveyor to submit a plan to the Certifier, certifying that structural works are in accordance with this consent.		✓					
B47	The Applicant must cause a Registered Surveyor to measure and mark: (a) prior to commencement of works - the positions of all footings/ foundations; and (b) at other stages of construction - any marks that are required by the Certifier, and provide information on the positions to the Certifier.	✓	✓					
B48	HOARDING A separate application under section 138 of the Roads Act 1993 is to be made to the relevant road authority to erect a hoarding and/or scaffolding in a public road and such application is to include: (a) architectural, construction and structural details of the design as well as proposed artwork; and (b) structural certification prepared and signed by an appropriately qualified practising structural engineer. Evidence of the issue of a Structural Works Inspection Certificate and structural certification will be required prior to the commencement of construction works on site, only as they relate to the specific works under section 138 of the Roads Acts 1993 required by condition B51.	As required	As required	As required	As required	As required		
B49	BARRICADE PERMIT Where construction/building works require the use of a public place including a road or footpath, approval under section 138 of the Roads Act 1993 for a Barricade Permit must be obtained prior to the commencement of works, only as they relate to the specific works under section 138 of the Roads Act 1993 required by condition B49. Details of the barricade construction, area of enclosure and period of work must be submitted to the satisfaction of the relevant road authority.	As required	As required	As required	As required	As required		
B50	ROAD OCCUPANCY LICENCE A Road Occupancy Licence (ROL) must be obtained from the relevant road authority under section 138 of the Roads Act 1993 for any activity that may impact on the operation of the road network. The ROL allows the Applicant to use a specified road space at approved times, provided certain conditions are met. The Applicant must allow a minimum of 10 working days for processing ROL applications. Traffic Control Plans are to accompany each ROL application(s) for any such activities.	As required	As required	As required	As required	As required		
B51	CONTAMINATION UNEXPECTED FINDS Prior to the commencement of works, an Unexpected Contamination Finds Protocol (UFP) prepared by a suitably qualified and experienced expert shall be prepared. The protocol should include detailed procedures for identifying and dealing with unexpected contamination, asbestos and other unexpected finds. The Applicant should ensure that the procedure includes details of who will be responsible for implementing the unexpected finds procedure and the roles and responsibilities of all parties involved. The UFP must be submitted to the satisfaction of Certifier. The UFP must be implemented for the duration of construction works. Details demonstrating compliance with the above requirements must be submitted to the Certifier. A copy of all the documentation outlined in the above requirements must be submitted to the Planning Secretary.	✓						
B52	HISTORICAL ARCHAEOLOGY – HERITAGE NSW A procedure for the management of unexpected relics and human remains must be developed in consultation with Heritage NSW. This procedure must: (a) be prepared in accordance with Heritage NSW guidelines and codes of practice. (b) include a hold point requiring the development of a revised historical archaeological assessment in the event an unexpected relic is identified. (i) The Archaeological Assessment must be prepared in accordance with the guideline Archaeological Assessment (1996) and Assessing Significance for Historical Archaeological Sites and Relics (2009) to inform and guide archaeological mitigation measures. (ii) If harm cannot be avoided in whole or part, an Archaeological Research Design and Excavation Methodology (ARDEM) with a nominated Excavation Director should also be prepared to guide any proposed excavations or salvage program. (iii) The Archaeological Assessment must be provided to the Secretary of the Department of Planning, Housing and Infrastructure for approval in consultation with Heritage NSW. (c) must be implemented for the duration of the project.	✓						
B53	All reasonable steps must be taken to avoid harm, modification of or impact to relics except as authorised by this approval.	✓	✓	✓	✓	✓		
B54	Keep a record of, and ensure all on-site workers receive suitable heritage inductions prior to carrying out any development activities on site.	✓	✓	✓	✓	✓		
B55	MARITIME UNEXPECTED FINDS – HERITAGE NSW A maritime specific Unexpected Finds Protocol (MUFP) is to be prepared by a suitably qualified and experienced maritime archaeologist as defined in the Australasian Institute for Maritime Archaeology Code of Ethics. The MUFP items must specifically include: (a) briefings of onsite works staff in recognition of maritime heritage items. (b) consideration of short and long term management, conservation, restoration, storage and interpretation of any significant maritime heritage items and how these aspects will be funded. (c) the possibility for redesign if significant maritime heritage items are discovered during works.	✓						
B56	ABORIGINAL CULTURAL HERITAGE MANAGEMENT PLAN - ACHMP Prior to the commencement of works, the Applicant must prepare an ACHMP for the development. This plan must: (a) be prepared by a suitably qualified and experienced person; (b) be prepared in consultation with the RAPS and reviewed by Heritage NSW (c) include a methodology for a test excavation and salvage excavation program with Aboriginal Stakeholder participation of sites to be impacted with consideration to understanding site characteristics, and local and regional archaeological context (d) include a description of the measures (and associated methodologies) that would be implemented for: (i) salvaging and relocating the Aboriginal heritage items located within the approved development footprint; (ii) include updated baseline mapping of the heritage items within and adjoining to the development disturbance area; (iii) include updated mapping of all areas that have been and will be subject to test excavations, and salvage excavations; (iv) include conservation options for the mitigation and avoidance to impacts AHIMS registered sites situated within and outside the project footprint; (v) include a procedure for assessing significance of Aboriginal Objects identified during the test excavations, and salvage excavation and ensure that the management and mitigation measures are considered for all sites, and with special consideration for those of high significance (vi) the long-term management of any Aboriginal heritage items or material collected during the test excavations or salvage works; (vii) ensuring workers on site receive suitable heritage inductions prior to carrying out any development on site, and that records are kept of these inductions; (viii) ongoing consultation with RAPs during the implementation of the ACHMP; (ix) preparing Aboriginal Site Impact Recording Form/s (ASIRFs) for all Aboriginal heritage sites following construction activities with ASIRFs to be submitted to the Aboriginal Heritage Information Management System (AHIMS) registrar. (e) include a contingency plan and reporting procedure including: (i) an Unexpected Heritage Finds and Human Remains Procedure prepared in relation to Aboriginal Cultural heritage, with these measures to be prepared in accordance with the guidelines and standards specified by Heritage NSW, be implemented for the duration of the project and to include the requirement to register any newly identified Aboriginal objects or sites in the AHIMS database. (f) include a program to monitor and report on the effectiveness of these measures and any heritage impacts of the project.	✓						
B57	Upon the completion of Aboriginal cultural heritage test and salvage excavations, an Aboriginal Cultural Heritage Excavation Report (s), prepared by a suitable qualified expert. The Aboriginal Cultural Heritage Excavation Report(s) must: (a) be prepared in accordance with the Guide to Investigation, assessing and reporting on Aboriginal cultural heritage in NSW, 2011 and the Code of Practice for Archaeological Investigation of Aboriginal Objects in New South Wales , 2010; and (b) document the results of the archaeological test excavations and any subsequent salvage excavations (with artefact analysis and identification of a final repository for finds) (c) The RAPs must be given a minimum of 28 days to consider the report and provide comments before the report is finalised. The final report must be provided to the Planning Secretary, Heritage NSW, Councils, and the relevant Local Aboriginal Land Council, and the RAPs within 24 months of the completion of the Aboriginal archaeological collections and excavations (both test and salvage).							✓
B58	TEMPORARY PROTECTION PLAN Prior to commencement of works, a temporary protection plan prepared by a suitably qualified and experienced consultant shall be submitted to the Certifier. The plan is to identify the potential risks and outlines measures to reduce the potential for damage to significant built, landscape and archaeological elements during site preparation and the works.	✓						
B59	HERITAGE CONSULTANT A suitably qualified and experienced heritage consultant is to be commissioned by the Applicant to provide detailed heritage advice to the project for its duration, including providing guidance to the construction documentation, the implementation of the conditions of consent and through the construction process. Written documentation to support the commission of the heritage consultant is to be submitted to the Certifier prior to the commencement of works.	✓	Maintained for duration of project	Maintained for duration of project	Maintained for duration of project	Maintained for duration of project		
B60	PROTECTION OF STREET TREES Prior to commencement of works, the street trees on the Worth Place frontage of the site are to be retained and physically protected in accordance with the Council's Urban Forest Technical Manual Note: The tree protection fencing is to remain in place and be maintained until all works have been completed, with no waste materials, washouts, equipment or machinery to be stored within the fenced area.	✓	Maintained for duration of project	Maintained for duration of project	Maintained for duration of project	Maintained for duration of project		
B61	CAR PARKING Prior to the commencement of above ground works, the Applicant must submit to the Certifier a Car Parking plan. The plan must demonstrate the provision in the adjacent Wright Lane carpark of the following: (a) a minimum of 6 disabled parking spaces; (b) a minimum of 2 car parking bays dedicated for use as Loading Zone bays; (c) a minimum of 4 car parking spaces to be dedicated for use as Short-term Parking bays; and (d) a minimum of 2 car parking spaces dedicated for use as Ride Share spaces The design of the on-site car parking and vehicular access is to comply with the relevant provisions of the latest version of AS/NZS 2890 -Parking facilities.		✓					
B62	ROADS ACT APPROVAL Prior to the commencement of works within the road reserve, a separate application is to be lodged, and consent obtained from Council for all works within the road reserve pursuant to Section 138 of the Roads Act 1993, or other satisfactory arrangements confirmed in writing from Council.					✓		

City Campus Student Accommodation SSDA Conditions of Consent Responsibility Matrix								
CONDITION	DESCRIPTION	CC1 - Inground Works	CC2 - Superstructure	CC3 - Façade	CC4 - Services and Finishes / Fitout	CC5 - Balance of Works	OC	Operation
B63	PUBLIC DOMAIN WORKS Prior to the commencement of Civic Lane public domain works, full details are to be provided to, and consent obtained, or other satisfactory arrangements confirmed in writing, from Council pursuant to Section 138 of the Roads Act 1993 for the following works to be designed and constructed by the Applicant within Civic Lane public road reserve and Worth Place, adjacent to the site, at no cost to Council and in accordance with Council's guidelines and design specifications: (a) a permanent shared path along the Civic Lane frontage of the student accommodation site and other associated works on Worth Place, up to the transition point located east of the proposed student accommodation building. The design details must include those works associated with that portion of the shared path located within the site. (b) a temporary shared path and other associated works from the eastern boundary (transition point) of the student accommodation site to the eastern end of the Newcastle City Campus in the Museum Precinct. (c) phase 1 works of the Civic Lane Concept Proposal as indicated by Council's notations on the Northrop drawing (CC2-C04.01 Rev 3) identified as 'Public Domain Works Plan-CN Mark-up Concept-dated 15 April 2025'. These works include, but are not limited to, a shared path ramp and footpath continuation at the intersection of Civic Lane and Worth Place, street lighting, kerb extension and streetscape improvements. (d) all the above works in Civic Lane and Worth Place must be designed and constructed generally in accordance with the requirements of 'Public Domain Works Plan-CN Mark-up Concept-dated 15 April 2025'. (e) all associated traffic and parking works. (f) the proposed driveway to the Loading Dock must be designed generally as identified on 'Public Domain Works-CN Mark-up Concept-15 April 2025 to enable both Medium Rigid vehicles and Small Rigid vehicles to drive forward in and reverse out. Plans of the vehicular turning movements of the above vehicles must be provided with the detailed design of Civic Lane. Engineering design plans and specifications for the works to be undertaken within the public road reserve are to be prepared by a practising professional engineer and associated relevant consultants with experience and competence in the related field, and in compliance with all relevant Australian and NSW standards, guidelines, and technical directions.					✓		
B64	FLOOD EMERGENCY RESPONSE PLAN Prior to the commencement of above ground works, the Applicant is to submit to the Certifier a Flood Emergency Response Plan for the construction phase of the development. It is to be prepared by a professional engineer, who is experienced in flood management. The plan is to include an education and awareness component for the workforce, detailed evacuation procedures to interface with the Bureau of Meteorology's flood warning system and the local State Emergency Services plan and provisions for any third parties likely to be involved. The flood emergency response plan is to describe the following components: (a) the flood emergency responses for the construction phase of the development; (b) likely flood behaviour (c) flood warning systems (d) an education awareness program (e) evacuation and evasion procedures (f) evacuation routes and flood refuges and flood warning system (g) flood preparedness and awareness procedures for employees and contractors Considerations are to include the full range of flood risks, the proposed use of the site, site access constraints and local area evacuation routes to high ground. The plan is to be aimed at self-directed evacuation or evasion to minimise the draw on limited State Emergency Services resources.		✓					
B65	FLOOD REFUGE Prior to the commencement of above ground works, the Applicant is to submit to the Certifier a plan prepared by a suitably qualified and experienced Civil Engineer showing an onsite flood refuge. The plan must: (a) demonstrate the level of the refuge is above the level of the Probable Maximum Flood Event; and (b) the design and/or suitability of the refuge is to be structurally certified by the engineer, ensuring that the building is able to withstand the hydraulic loading due to flooding from the Probable Maximum Flood.		✓					
PART C DURING CONSTRUCTION								
C1	SITE NOTICE A site notice(s) shall be prominently displayed at the boundaries of the Site for the purposes of informing the public of project details including, but not limited to the details of the Builder, Certifier and Structural Engineer. The notice(s) is to satisfy all but not be limited to, the following requirements: (a) the notice is to be able to be read by the general public; (b) the notice is to be rigid, durable and weatherproof and is to be displayed throughout the works period; (c) the approved hours of work, the name of the site/project manager, the responsible managing company (if any), its address and 24-hour contact phone number for any inquiries, including construction/noise complaint are to be displayed on the site notice; and (d) the notice(s) is to be mounted at eye level on the perimeter hoardings/fencing and is to state that unauthorised entry to the Site is not permitted.	✓	✓	✓	✓	✓		
C2	APPROVED PLANS TO BE ON-SITE A copy of the approved and certified plans, specifications and documents incorporating conditions of approval and certification shall be kept on the Site at all times and shall be readily available to any officer of the Department, Council or the PCA.	✓	✓	✓	✓	✓		
C3	CONTACT TELEPHONE NUMBER The Applicant shall ensure that the 24-hour contact telephone number is continually attended by a person with authority over the works for the duration of the development.	✓	✓	✓	✓	✓		
C4	CHECKING FLOOR LEVELS During building work, certification is to be prepared by a Registered Surveyor and submitted to the Certifier at the following stages of construction: (a) on completion of ground floor construction, confirming that the floor levels are in accordance with the approved levels. (b) on completion of each subsequent floor level, confirming that the floor levels are in accordance with the approved levels. (c) when the roof has been completed, confirming that the building does not exceed the approved levels.		✓	✓	✓			
C5	SETTING OUT OF STRUCTURES The building shall be set out by a registered surveyor to verify the correct position of the structure in relation to property boundaries and the approved alignment levels. The registered surveyor shall submit a plan to the Certifier, certifying that structural works are in accordance with the approved development application.	✓	✓					
C6	HOURS OF CONSTRUCTION Construction, including the delivery of materials to and from the site, may only be carried out between the following hours: (a) between 7:00 am and 6:00 pm, Mondays to Fridays inclusive; and (b) between 8:00 am and 1:00 pm, Saturdays.	✓	✓	✓	✓	✓		
C7	No work may be carried out on Sundays or public holidays.	✓	✓	✓	✓	✓		
C8	Activities may be undertaken outside of these hours if required: (a) by the Police or a public authority for the delivery of vehicles, plant or materials; or (b) in an emergency to avoid the loss of life, damage to property or to prevent environmental harm. (c) where the works are inaudible at the nearest sensitive receivers; or (d) where a variation is approved in advance in writing, by the Planning Secretary or their nominee, if appropriate justification is provided for the works.	✓	✓	✓	✓	✓		
C9	Notification of such activities must be given to affected residents before undertaking the activities or as soon as is practical afterwards.	✓	✓	✓	✓	✓		
C10	Rock breaking, rock hammering, sheet piling, pile driving and similar activities may only be carried out between the following hours: (a) 9.00 am to 12.00 pm, Monday to Friday; (b) 2.00 pm to 5.00 pm Monday to Friday; and (c) 9.00 am to 12.00 pm, Saturday.	✓	✓	✓	✓	✓		
C11	IMPLEMENTATION OF MANAGEMENT PLANS The Applicant shall ensure that the requirements of the CEMP, CPTMP, CNVMP, CWMP, AQMP, GMP, UFP and MUFP required by Parts B and C of this consent are implemented during construction.	✓	✓	✓	✓	✓		
C12	CONSTRUCTION NOISE AND VIBRATION MANAGEMENT The development must be constructed with the aim of achieving the construction noise management levels detailed in the Interim Construction Noise Guideline (Department of Environment and Climate Change, 2009). All feasible and reasonable noise mitigation measures shall be implemented and any activities that could exceed the construction noise management levels shall be identified and managed in accordance with the CEMP and CNVMP.	✓	✓	✓	✓	✓		
C13	If the noise from a construction activity is substantially tonal or impulsive in nature (as described in Chapter 4 of the NSW Industrial Noise Policy), 5 dB(A) must be added to the measured construction noise level when comparing the measured noise with the construction noise management levels.	✓	✓	✓	✓	✓		
C14	Heavy vehicles and oversized vehicles must not queue or idle on Civic Lane or Worth Place outside of construction zones awaiting access to the site.	✓	✓	✓	✓	✓		
C15	The Applicant must schedule intra-day 'respite periods' for construction activities predicted to result in noise levels in excess of the "highly noise affected" levels, including the addition of 5 dB to the predicted levels for those activities identified in the Interim Construction Noise Guideline as being particularly annoying to noise sensitive receivers.	✓	✓	✓	✓	✓		
C16	Wherever practical, and where sensitive receivers may be affected, piling activities are completed using bored piles. If driven piles are required, they must only be installed where outlined in the CEMP.	✓	✓	✓	✓	✓		
C17	Vibration caused by construction at any residence or structure outside the subject site must be limited to: (a) for structural damage vibration to buildings (excluding heritage buildings), British Standard BS 7385 Part 2-1993 Evaluation and Measurement for Vibration in Buildings; (b) for structural damage vibration to heritage buildings, German Standard DIN 4150 Part 3 Structural Vibration in Buildings Effects on Structure; (c) for human exposure to vibration, the evaluation criteria presented in British Standard BS 6472- Guide to Evaluate Human Exposure to Vibration in Buildings (1Hz to 80 Hz) for low probability of adverse comment; and (d) these limits apply unless otherwise outlined in the CNVMP.	✓	✓	✓	✓	✓		
C18	Vibratory compactors must not be used within 30 metres of residential or heritage buildings unless vibration monitoring confirms compliance with the vibration criteria specified above. These limits apply unless otherwise outlined in the project specific CNVMP required by this consent.	✓	✓	✓	✓	✓		
C19	EROSION AND SEDIMENT CONTROL All erosion and sediment control measures are to be effectively implemented and maintained at or above design capacity for the duration of the construction works and until such time as all ground disturbed by the works has been stabilised and rehabilitated so that it no longer acts as a source of sediment.	✓	✓	✓	✓	✓		
C20	DISPOSAL OF SEEPAGE AND STORMWATER Any seepage or rainwater collected on-site during construction shall be either re-used or disposed of, so as not to cause pollution. Seepage or rainwater shall not be pumped to the street stormwater system unless separate prior approval is given in writing by Council.	✓	✓	✓	✓	✓		
C21	LOADING AND UNLOADING DURING CONSTRUCTION The following requirements apply: (a) all loading and unloading associated with demolition and construction must be accommodated on-site; (b) a Works Zone is required if loading and unloading is not possible on site. If a Works Zone is warranted an application must be made to the relevant road authority at least 8 weeks prior to commencement of works on the site. Consent for a Works Zone may be given for a specific period and certain hours of the days to meet the particular need for the site for such facilities at various stages of construction. The consent will be reviewed periodically for any adjustment necessitated by the progress of the construction activities	✓	✓	✓	✓	✓		
C22	COVERING OF LOADS All vehicles involved in the excavation and / or demolition process and departing from the property with materials, spoil or loose matter must have their loads fully covered before entering the public roadway.	✓	✓	✓	✓	✓		
C23	VEHICLE CLEANSING Prior to the commencement of work, suitable measures are to be implemented to ensure that sediment and other materials are not tracked onto the roadway by vehicles leaving the Site. It is an offence to allow, permit or cause materials to pollute or be placed in a position from which they may pollute waters.	✓	✓	✓	✓	✓		
C24	HOARDING/FENCING REQUIREMENTS The following hoarding requirements must be complied with: (a) no third-party advertising, unless associated with State or Commonwealth Funding of the development or development deeds (such as logos of such associated stakeholders), is permitted to be displayed on the subject hoarding/fencing; and (b) the removal of all graffiti from any construction hoarding/fencing or the like within the construction area within 48 hours of its application.	✓	✓	✓	✓	✓		
C25	WASTE MANAGEMENT Notwithstanding the CWMP referred to in condition B43, the Applicant must ensure that: (a) all waste generated by the development is classified and managed in accordance with the EPA's Waste Classification Guidelines Part 1: Classifying Waste 2009; (b) all waste generated by the development is treated and/or disposed of at a facility that has sufficient capacity to and may lawfully accept that waste; (c) waste (including litter, debris or other matter) is not caused or permitted to enter the waters of the nearby harbour; (d) any vehicle used to transport waste or excavation spoil from the site is covered before leaving the premises; (e) the wheels of any vehicle, trailer or mobilised plant leaving the site and cleaned of debris prior to leaving the premises; and (f) concrete waste and rinse water are not disposed of on the site and are not caused or permitted to enter the waters of the nearby harbour.	✓	✓	✓	✓	✓		
C26	STOCKPILE MANAGEMENT The Applicant must ensure that: (a) stockpiles of excavated material do not exceed 4 metres in height; (b) stockpiles of excavated material are constructed and maintained to prevent cross contamination; and (c) suitable erosion and sediment controls are in place for stockpiles.	✓	✓	✓	✓	✓		
C27	DUST CONTROL MEASURES Adequate measures shall be taken to prevent dust from affecting the amenity of the neighbourhood during construction. In particular, the following measures should be adopted: (a) physical barriers shall be erected at right angles to the prevailing wind direction or shall be placed around or over dust sources to prevent wind or activity from generating dust emissions; (b) earthworks and scheduling activities shall be managed to coincide with the next stage of development to minimise the amount of time the site is left cut or exposed; (c) all materials shall be stored or stockpiled at suitable locations and stockpiles shall be maintained at manageable sizes which allow them to be covered, if necessary, to control emissions of dust and/or VOCs/odour; (d) the surface should be dampened slightly to prevent dust from becoming airborne but should not be wet to the extent that run-off occurs; (e) all vehicles carrying spoil or rubble to or from the site shall at all times be covered to prevent the escape of dust or other material; (f) all equipment wheels shall be washed before exiting the site using manual or automated sprayers and drive-through washing bays; (g) gates shall be closed between vehicle movements and shall be fitted with shade cloth; and (h) cleaning of footpaths and roadways shall be carried out regularly.	✓	✓	✓	✓	✓		
C28	NO OBSTRUCTION OF THE PUBLIC WAY The public way must not be obstructed by any materials, vehicles, refuse skips or the like, under any circumstances. Non-compliance with this requirement will result in the issue of a notice by the Planning Secretary to stop all work on site.	✓	✓	✓	✓	✓		
C29	DAMAGE TO THE PUBLIC WAY Any damage to the public way, including trees, footpaths, kerbs, gutters, road carriageway and the like, must immediately be made safe and functional by the Applicant.	✓	✓	✓	✓	✓		
C30	ASBESTOS AND HAZARDOUS WASTE REMOVAL Any hazardous materials, including asbestos, must be identified before demolition work commences and be removed in a safe manner.	✓	✓	✓	✓	✓		
C31	All materials requiring removal from the site must be classified in accordance with Waste Classification Guidelines (NSW EPA, 2014). The Applicant must ensure that demolition works are undertaken so that cross-contamination of the site does not occur.	✓	✓	✓	✓	✓		
C32	Removal of asbestos and other hazardous building materials must be undertaken by a suitably licensed contractor and an asbestos clearance certificate must be provided before waste classification, disposal or site validation is undertaken.	✓	✓	✓	✓	✓		
C33	The Applicant must implement the UFP (see condition B54) for the duration of construction. Should any new information come to light during demolition or construction works which has the potential to alter previous conclusions about site contamination, the Department must be immediately notified and works must cease. Works must not recommence on site until the Department confirms works can recommence.	✓	✓	✓	✓	✓		

City Campus Student Accommodation								
SSDA Conditions of Consent Responsibility Matrix								
CONDITION	DESCRIPTION	CC1 - Inground Works	CC2 - Superstructure	CC3 - Façade	CC4 - Services and Finishes / Fitout	CC5 - Balance of Works	OC	Operation
C34	SAFework NSW REQUIREMENTS To protect the safety of work personnel and the public, the work site must be adequately secured to prevent access by unauthorised personnel, and work must be conducted at all times in accordance with relevant SafeWork NSW requirements.	✓	✓	✓	✓	✓		
C35	ABORIGINAL HERITAGE - ACHAR All reasonable steps must be taken so as no to harm, modify or other impact Aboriginal objects except as authorised by this approval.	✓	✓	✓	✓	✓		
C36	The Registered Aboriginal Parties (RAPs) must be kept informed about the SSD. The RAPs must continue to be provided with the opportunity to be consulted about the Aboriginal Cultural heritage management requirements of the SSD.	✓	✓	✓	✓	✓		
C37	WATER SUPPLY, TAKE AND LICENSING – DCCEEW – Water Should groundwater be intercepted, a water access license (WAL) must be obtained prior to any take occurring unless an exemption applied under the Water Management (General) Regulation 2018.	As required	As required	As required	As required	As required		
C38	EMERGENCY MANAGEMENT The Applicant must prepare and implement awareness training for employees and contractors, including locations of assembly points and evacuation routes, for the duration of construction.	✓	✓	✓	✓	✓		
C39	LOCOMOTIVE TURNTABLE – HERITAGE NSW The location of the turntable is to be accurately mapped and the AHD level of the top of the perimeter wall is to be measured. This information is to be used in the development of the landscape design to avoid potential impacts.					✓		
C40	There are to be no physical impacts to the locomotive turntable as result of the proposed works. This includes impacts related to paving and bedding, soft landscaping, structures and footings, and services.	✓	✓	✓	✓	✓		
C41	An exclusion zone is to be established around the turntable during construction to protect it from damage. The establishment of the exclusion zone is to be included in any Construction Environmental Management Plan (CEMP) for the site.	✓	✓	✓	✓	✓		
C42	The location of the locomotive turntable should be accurately identified in the finished works to help prevent future damage to the structure.					✓		
C43	Interpretation of the locomotive turntable is to be developed in consultation with an experienced heritage practitioner and is to be based on accurate historical information.					✓		
C44	HISTORICAL ARCHAEOLOGY – HERITAGE NSW Where works to identify and protect the location of the locomotive turntable require subsurface investigation, these are to be monitored by a suitably qualified historical archaeologist to ensure that the locomotive turntable is not impacted. An Archaeological Method Statement to guide archaeological monitoring and specify measures which will be implemented to protect the turntable is to be included as a part of a Construction Environmental Management Plan (CEMP) for the site. The CEMP is to be provided to the Department for approval prior to the commencement of works within the area of influence of the locomotive turntable.					✓		
C45	HERITAGE INTERPRETATION PLAN Following the completion of the archaeology works, a detailed Heritage Interpretation Plan (HIP) prepared by a suitably experienced heritage interpretation practitioner shall be submitted to the Certifier. The HIP must: (a) be in accordance with the Heritage Council's 'Interpreting Heritage Places and Items Guidelines' (2005); (b) build upon the themes and opportunities identified in the Umwelt Heritage Interpretation Strategy (18 June 2024); (c) make allowance for the display of any potential archaeology uncovered during the works; and (d) interpret the multiple uses and history of the various heritage buildings and elements on the site in a way that is engaging, informative and readily accessible to the majority of visitors.					✓		
PART D PRIOR TO OCCUPATION OR COMMENCEMENT OF USE								
D1	NOTICE OF OCCUPATION The date of commencement of the occupation of the development must be notified to the Department in writing, at least one month before occupation. If the operation of the development is to be staged, the Department must be notified in writing at least one month before the commencement of each stage, of the date of commencement and the development to be carried out in that stage.						✓	
D2	HEIGHT CERTIFICATION A Registered Surveyor is to certify that the height of the building does not exceed RL 37.53m AHD. Details shall be provided to the Certifier demonstrating compliance with this condition prior to occupation or commencement of use.						✓	
D3	OPERATIONAL PLAN OF MANAGEMENT Prior to the occupation or commencement of use, a detailed Operational Plan of Management (OPM) shall be submitted to the Certifier. The OPM must be prepared in consultation with Council. The OPM must address (but not be limited to): (a) management of communal areas and open spaces (see conditions E2 to E6); (b) loading and unloading, security and staff management, emergency management/evacuation and incident response protocols, occupational health and safety, waste management, water management, wayfinding and signage, and lighting; (c) tenant induction and education programs regarding use of the building's environmental systems; (d) community consultation and complaint management; and (e) management of student move-in and move-outs.						✓	
D4	TREE PLANTING, LANDSCAPING AND PUBLIC DOMAIN WORKS All tree planting, landscaping and public domain works approved by condition A2, must be completed in accordance with the approved plans, including the detailed landscape plan prior to occupation or commencement of use.						✓	
D5	Prior to occupation or commencement of use, structural and waterproofing certifications for the green roof are to be submitted to and approved by the Certifier						✓	
D6	ROAD DAMAGE The cost of repairing any damage caused to Council or other public authority's assets in the vicinity of the site as a result of construction works associated with the approved development, is to be met in full by the Applicant/developer prior to the commencement of use.						✓	
D7	UTILITY PROVIDERS Prior to occupation or commencement of the use, written advice shall be obtained from the relevant water supply authority, wastewater disposal authority, electricity supply authority, an approved telecommunications carrier and an approved gas carrier (where relevant) stating that satisfactory arrangements have been made to ensure provision of adequate services.						✓	
D8	POST-CONSTRUCTION DILAPIDATION REPORT Prior to occupation or commencement of use: (a) The Applicant shall engage a suitably qualified person to prepare a post-construction dilapidation report at the completion of the construction works. This report to ascertain whether the construction works created any structural damage to adjoining buildings, infrastructure and roads. (b) The report is to be submitted to the Certifier. In ascertaining whether adverse structural damage has occurred to adjoining buildings, infrastructure and roads, the Certifier must: (i) compare the post-construction dilapidation report with the pre-construction dilapidation report required by these conditions and (ii) have written confirmation from the relevant authority that there is no adverse structural damage to their infrastructure and roads. (c) A copy of this report is to be forwarded to the Council and the Planning Secretary and each of the affected property owners.						✓	
D9	STRUCTURAL INSPECTION CERTIFICATE A Structural Inspection Certificate or a Compliance Certificate must be submitted to the satisfaction of the Certifier prior to occupation or use of the premises. A copy of the Certificate with an electronic set of final drawings (contact approval authority for specific electronic format) shall be submitted to the approval authority and the Council after: (a) the site has been periodically inspected and the Certifier is satisfied that the Structural Works is deemed to comply with the final design drawings; and (b) the drawings listed on the Inspection Certificate have been checked with those listed on the final Design Certificate/s.						✓	
D10	ECOLOGICALLY SUSTAINABLE DEVELOPMENT Unless otherwise agreed by the Planning Secretary, within 12-months of commencement of operation, Green Star certification is obtained demonstrating the development achieves a minimum 4-star (or aspirational 5-star) Green Star Buildings v1 rating. If required to be obtained, evidence of the certification must be provided to the Certifier and the Planning Secretary.						✓	
D11	MECHANICAL VENTILATION Following completion, installation and testing of all the mechanical ventilation systems, the Applicant shall provide evidence to the satisfaction of the Certifier, prior to occupation or commencement of use, that the installation and performance of the mechanical systems complies with: (a) the NCC; (b) Australian Standard AS1668 and other relevant codes; (c) the development consent and any relevant modifications; and, (d) any dispensation granted by Fire and Rescue NSW.						✓	
D12	CRIME PREVENTION THROUGH ENVIRONMENTAL DESIGN Prior to occupation or commencement of use, evidence shall be submitted to the Certifier demonstrating the recommendations of the CPTED Report, prepared by Ethos Urban, dated 22 November 2024 have been implemented.						✓	
D13	WIND MITIGATION MEASURES Prior to occupation or commencement of use, evidence shall be submitted to the Certifier demonstrating compliance with all wind mitigation recommendations of the Pedestrian Wind Environment Assessment, prepared by Windtech Consultants dated 15 July 2024.						✓	
D14	FIRE SAFETY CERTIFICATION Prior to the occupation or commencement of use of the development, a Fire Safety Certificate shall be obtained for all the Essential Fire or Other Safety Measures forming part of this consent. A copy of the Fire Safety Certificate must be submitted to the relevant authority and be prominently displayed in the building.						✓	
D15	SANITARY FACILITIES FOR DISABLED PERSONS Prior to occupation or commencement of the use, details must be provided to the Certifier demonstrating that the provision of sanitary facilities for disabled persons within the premises complies with Section F2.4 of the NCC and condition B34.						✓	
D16	WASTE AND RECYCLING COLLECTION Prior to occupation or commencement of use, the building owner must ensure that there is a contract with a licensed contractor for the removal of all trade waste. No garbage is to be placed on the public way e.g. the roadways, footpaths, through-site link and reserves at any time.						✓	
D17	Prior to occupation or commencement of use, the Certifier must ensure that waste handling works have been completed in accordance with the OWMP.						✓	
D18	ACOUSTIC COMPLIANCE Prior to occupation or commencement of, evidence shall be submitted to the Certifier demonstrating compliance with all noise mitigation measures required under condition B22 to ensure the development achieves compliance with the requirements of the NSW Industrial Noise Policy and other guidelines applicable to the development.						✓	
D19	EXTERNAL WALLS AND CLADDING FLAMMABILITY Prior to occupation or commencement of use, evidence shall be submitted to the Certifier demonstrating all external walls of the building, including cladding, comply with the relevant requirements of the NCC, consistent with the requirements of condition B18.						✓	
D20	PROTECTION OF PUBLIC INFRASTRUCTURE Unless the Applicant and the applicable authority agree otherwise, the Applicant must: (a) repair, or pay the full costs associated with repairing, any public infrastructure that is damaged by carrying out the development; and (b) relocate, or pay the full costs associated with relocating any infrastructure that needs to be relocated as a result of the development						✓	
D21	REFLECTIVITY Prior to occupation or commencement of use, evidence shall be submitted to the Certifier demonstrating that the building materials have a maximum normal specular reflectivity of visible light of 20 per cent or consist of alternate materials / mitigation measures that so that the facades of the building do not result in glare that causes any discomfort or threatens the safety of pedestrians or drivers.						✓	
D22	VERIFICATION OF ACOUSTIC PERFORMANCE – PORT AUTHORITY Prior to occupation or commencement of use, verification be provided to the consent authority that the development has achieved its required acoustic performance for all living/dining and sleeping areas.						✓	
D23	GREEN TRAVEL PLAN – TNSW Prior to occupation or commencement of use, the Green Travel Plan (prepared by SECA Solutions, version Ver04, dated 11 July 2024) shall be updated to include: (a) An Implementation Plan section with committed actions ready for implementation from the first day of occupancy; and (b) A Travel Survey included as a separate appendix. The survey should be included in the Implementation Plan and distributed three (3) months post-occupancy to both staff and students. The survey should include questions to obtain residential postcodes to identify origin and destination patterns to inform strategies that aim to increase the use of public and active transport by staff and visitors driving to and from the site. Questions regarding interest in initiatives promoting sustainable transport should also be used here; and (c) Additional information about walking and cycling routes to/from and around the site; and (d) A website link to the Travel Access Guides (TAGs) as referred to in condition D26 shall be included as an appendix in the GTP. The updated Green Travel Plan shall be provided to and endorsed by TNSW. A copy of the final plan shall be submitted to the Planning Secretary. Details demonstrating compliance with these requirements must be submitted to the Certifier prior to occupation or commencement of use.						✓	
D24	The GTP will need to be appropriately funded and otherwise resourced, by the applicant, for a period of at least 5 years, or via an appropriate appointed entity. This will include ongoing travel demand initiatives in the Implementation Plan that will require resourcing. This is in recognition that any travel demand management interventions will need to be significant in scale to be effective.						✓	
D25	A Travel Plan Coordinator (TPC) shall be appointed for the life of the development who will manage the GTP from the first day of occupancy. Further consideration should also be given to having other staff involved to ensure the GTP is adequately monitored and evaluated, as well as implementing strategies if the TPCs change over the lifecycle of the development.						✓	
D26	TRANSPORT ACCESS GUIDE – TNSW Prior to occupation or commencement of use a Transport Access Guide must be prepared in consultation with TNSW. The Transport Access Guide shall include the following: (a) Additional information about service routes and timetables for buses, light rail, and trains to and from the site. (b) Additional information about service routes and timetables for university shuttle buses to and from the site. (c) Promotes bike parking and End of Trip facilities (EoT) such as showers, lockers and change rooms. (d) Does not promote parking areas where staff, students and visitors can park. (e) Suitable nearby drop-off/pick-up locations; and (f) Identify areas where drop-off/pick-up is prohibited and instruct visitors to avoid use of these areas; and (g) Suitable nearby Taxi Zones. The Travel Access Guide shall be provided to and endorsed by TNSW. A copy of the final plan shall be submitted to the Planning Secretary. Details demonstrating compliance with these requirements must be submitted to the Certifier prior to occupation or commencement of use.						✓	
D27	NO OBSTRUCTIONS – PUBLIC DOMAIN All public footways and paths of travel must be free from obstructions. If services are required to be relocated to clear paths of travel, then this must be undertaken at the developer's expense. All obstructions are to be removed prior to occupation or commencement of use.						✓	

City Campus Student Accommodation SSDA Conditions of Consent Responsibility Matrix

CONDITION	DESCRIPTION	CC1 - Inground Works	CC2 - Superstructure	CC3 - Façade	CC4 - Services and Finishes / Fitout	CC5 - Balance of Works	OC	Operation
D28	UTILITIES AND SERVICES – HUNTER WATER Prior to the commencement of operation, the Applicant must obtain a Compliance Certificate for water and sewerage infrastructure servicing of the site under section 50 of the Hunter Water Corporation Act 1991. The proponent is required to submit an application for Development Assessment (Section 50) for the proposed development in accordance with Section 49 of the Hunter Water Act 1991 (the Act) via the Hunter Water Self Service Portal (https://selfservice.hunterwater.com.au/). A Compliance Certificate will be issued under Section 50 of the Act for the proposed development once Hunter Water's specific requirements have been satisfied, and this Compliance Certificate must be submitted to the Certifier prior to commencement of works. The proponent is responsible for ensuring that any development staging is clearly defined in the development consent in order to allow the release of Section 50 Compliance Certificates for each development stage and, if required, the associated staged delivery of water and sewer infrastructure.						✓	
D29	DEVELOPER CONTRIBUTIONS Prior to occupation, the Certifier must provide a copy of the documentation to the Planning Secretary which confirms that there are no outstanding infrastructure contributions or levies.						✓	
D30	OUTDOOR LIGHTING Prior to occupation, the Applicant must submit evidence, from a suitably qualified practitioner to the Certifier, which demonstrates that all outdoor lighting within the site complies with, where relevant, AS/NZ1158.3: 1999 Pedestrian Area (Category P) Lighting and AS4282: 1997 Control of the Obtrusive Effects of Outdoor Lighting.						✓	
D31	STUDENT ACCOMMODATION AFFORDABILITY AND SUPPLY STRATEGY Prior to occupation or commencement of use, the Applicant must submit to the Certifier an Approach to Providing Affordable Student Accommodation statement. The Approach statement is to address the following at a minimum: (a) accommodation demand and supply analysis with benchmarking against student accommodation and other forms of accommodation typically occupied by students; (b) affordable student accommodation analysis trends and statistics associated with student demand and affordability price point for the University of Newcastle students; (c) the mechanisms deployed by the University to support affordable student housing; (d) confirmation of current student accommodation portfolio including age, price point, type of facility and details of future planned student accommodation development; and (e) typical student income (including government benefits) and accommodation costs as a proportion of that income.						✓	
D32	HERITAGE INTERPRETATION PLAN The Heritage Interpretation Plan required by Condition C45 must be implemented prior to occupation or commencement of use.						✓	
D33	SECTION 88B INSTRUMENT - PERMANENT SHARED PATH Prior to occupation or commencement of use, a notation is to be made on a survey plan and accompanying instrument under Section 88B of the Conveyancing Act 1919. It is to set out the terms of a required right of carriageway benefiting Newcastle City Council and the general public over the permanent shared path along the Civic Lane frontage of the student accommodation site up to the transition point located east of the proposed student accommodation building. The plan and instrument are to detail that Newcastle City Council and the general public can pass and repass without any costs, and such must not burden Council or the general public for any risks, liability and maintenance responsibility and must be accessible at all times without any restrictions.						✓	
D34	SECTION 88B INSTRUMENT – TEMPORARY SHARED PATH Prior to occupation or commencement of use, a notation is to be made on a survey plan and accompanying instrument under Section 88B of the Conveyancing Act 1919. It is to set out the terms of a required right of carriageway benefiting Newcastle City Council and the general public over the temporary shared path from the eastern boundary (transition point) of the student accommodation site to the eastern end of the Newcastle City Campus in the Museum Precinct. The plan and instrument are to detail that Newcastle City Council and the general public can pass and repass without any costs, and such must not burden council or the general public for any risks, liability and maintenance responsibility and must be accessible at all times without any restrictions. Note: i) Council in addition to the owner of any land benefited by the easement is to be a party whose consent is needed to release or vary easements or positive covenants. ii) Council will not withhold consent to release the positive covenants or easements in respect of temporary shared path subject to adequate alternate measures being provided.						✓	
D35	STORMWATER WORKS AS EXECUTED Prior to occupation or commencement of use, a copy of the approved stormwater drainage design plans with 'work as executed' levels indicated, must be submitted to the Certifier and to Council. The plans must be prepared by a Practising Professional Engineer or Registered Surveyor experienced in the design of stormwater drainage systems.						✓	
D36	WATER MANAGEMENT MEASURES COMPLETION Prior to occupation or commencement of use, the water management measures as indicated on the submitted plans and Statement of Environmental Effects and/or as modified under the terms of this consent are to be implemented and the nominated fixtures and appliances are to be installed and operational.						✓	
D37	CARPARKING Prior to occupation or commencement of use, allocated car parking within the Wright Lane Carpark is to be provided generally in accordance with the approved plans except as otherwise provided by the conditions of consent.						✓	
D38	PUBLIC DOMAIN WORKS The public domain works required by Condition B66 must be constructed and completed prior to occupation or commencement of use or otherwise agreed between Council and the applicant.						✓	
D39	BICYCLE PARKING AND END OF TRIP FACILITIES Prior to the occupation, details demonstrating compliance with the following requirements for secure bicycle parking and end-of-trip facilities must be submitted to the satisfaction of the Certifier: (a) a minimum of 90 bicycle parking spaces are to be provided internally for students and staff (including retail staff); (b) minimum of 23 bicycle loops (capable of securing 46 bicycles) are to be provided externally for students and staff; (c) the layout, design and security of all bicycle facilities must comply with the minimum requirements of Australian Standard AS 2890.3 – 2015; (d) the provision of end-of-trip facilities; (e) appropriate pedestrian and cyclist advisory signs are to be provided; and (f) all works/regulatory signposting associated with the proposed developments shall be at no cost to the relevant roads authority.						✓	
D40	FLOOD EMERGENCY RESPONSE PLAN – OPERATIONAL The Prior to the occupation or commencement of use, the Applicant is to submit to the Certifier a Flood Emergency Response Plan for the operational phase of the development. It is to be prepared by a professional engineer, who is experienced in flood management. The plan is to include an education and awareness component for the workforce, detailed evacuation procedures to interface with the Bureau of Meteorology's flood warning system and the local State Emergency Services plan and provisions for any third parties likely to be involved. The flood emergency response plan is to describe the following components: (a) the flood emergency responses for the operational phase of the development; (b) likely flood behaviour; (c) flood warning systems; (d) an education awareness program; (e) evacuation and evasion procedures; (f) evacuation routes and flood refuges and flood warning system; and (g) flood preparedness and awareness procedures for residents, visitors, staff and the like. Considerations are to include the full range of flood risks, the proposed use of the site, site access constraints and local area evacuation routes to high ground. The plan is to be aimed at self-directed evacuation or evasion to minimise the draw on limited State Emergency Services resources.						✓	
PART E POST OCCUPATION OPERATIONAL								
E1	OPERATIONAL PLAN OF MANAGEMENT The OPM (see condition D3) and all relevant plans must be fully implemented during use of the premises.							✓
E2	OPERATIONAL RESTRICTIONS The use of the communal facilities, including the rooftop terrace on level 1 is restricted to staff, residents and their guests.							✓
E3	Amplified noise/music is prohibited within external terraces and only low-level background music is permitted in internal communal areas.							✓
E4	Alcohol is prohibited to be consumed within the building, except within student rooms and the internal communal areas.							✓
E5	Internal speakers must not be placed to direct the playing of music towards the public domain or outdoor areas associated with the premises.							✓
E6	Noise associated with the operation of the development shall not give rise to the transmission of "offensive noise" as defined in the Protection of the Environment Operations Act 1997.							✓
E7	NOISE CONTROL – PLANT AND MACHINERY Noise associated with the operation of any plant, machinery or other equipment on the site, shall not give rise to any one or more of the following: (a) transmission of "offensive noise" as defined in the Protection of the Environment Operations Act 1997 to any place of different occupancy; (b) a sound pressure level at any affected residential property that exceeds the background (LA90, 15 minute) noise level by more than 5dB(A). The background noise level must be measured in the absence of noise emitted from the premises. The source noise level must be assessed as a LAeq, 15 minute; and (c) notwithstanding compliance with (1) and (2) above, the noise from mechanical plant associated with the premises must not exceed 5dB(A) above the background noise level between the hours of 12.00 midnight and 7.00 am.							✓
E8	LOADING AND UNLOADING All loading and unloading operations associated with the site must be carried out: (a) in a manner so as not to cause inconvenience to the public or detrimentally impact the amenity of the locality.							✓
E9	WASTE MANAGEMENT Waste Management shall be undertaken in accordance with the OWMP.							✓
E10	NO OBSTRUCTION OF THE PUBLIC WAY The public way must not be obstructed by any materials, waste, vehicles, refuse, skips or the like under any circumstances.							✓
E11	OUTDOOR FURNITURE Lightweight furniture is not permitted within communal open space areas unless securely attached to the floor slab. Use of loose glass-tops and lightweight sheets or covers is not permitted.							✓
E12	ANTI-GRAFFITI Where possible all ground level surfaces are to be treated with anti-graffiti coating to minimise the potential of defacement. In addition, any graffiti evident on the exterior facades and visible from a public place is to be removed within 48 hours.							✓
E13	PLAN OF MANAGEMENT FOR LANDSCAPE MAINTENANCE Within six months of the issue of occupation, a Plan of Management for the ongoing maintenance of landscaped areas and tree planting is to be prepared and adopted by the operator of the student accommodation.							✓
E14	TRANSPORT ACCESS GUIDE The Transport Access Guide shall be implemented and maintained by the operator of the student accommodation and be made available to staff, guests, clients, customers, and visitors at all times.							✓
E15	MAINTENANCE OF TREES ON SITE Tree maintenance must be implemented and complied with immediately following tree planting, and until the tree reaches the required minimum height limits.							✓
E16	Maintenance includes watering, weeding, removal of rubbish from tree bases, pruning (in accordance with AS4373-2007), fertilising, pest and disease control and any other operations required to maintain a healthy robust tree.							✓
E17	MAINTENANCE OF LANDSCAPING Landscaping in communal areas and level 1 external terrace must be maintained in accordance with the respective maintenance plans.							✓
E18	STREET LEVEL FAÇADE No opaque glass, film or security roller doors are permitted at any time on any part of the façade that faces the public domain at street level except for any signage, fixture, feature or the like provided as part of AS 1428.1 Design for access and mobility.							✓
E19	OPERATION OF PLANT AND EQUIPMENT All plant and equipment used on site, or to monitor the performance of the development, must be: (a) maintained in a proper and efficient condition; and (b) operated in a proper and efficient manner.							✓
E20	CAR PARKING During occupation and ongoing use, the proposed 14 allocated parking bays within the adjacent Wright Lane carpark as approved under this development are to be made available for their intended uses until further developments commence under the site's approved Concept Plan (SSD-9262). The utilisation of these spaces will be monitored by the applicant to assist in providing appropriate long-term amenity as the City Campus is further developed.							✓
E21	SITE MAINTENANCE During occupation and ongoing use of the site and student accommodation building, the driveway crossing associated with the service/loading bay, parking areas and stormwater management system are to be properly maintained for the life of the development.							✓
E22	LOADING AND UNLOADING During occupation and ongoing use, vehicles are to be loaded or unloaded standing wholly within the premises and within loading bays designated on the approved plans or as otherwise provided in accordance with the conditions of this consent and under no circumstances are vehicles to be loaded or unloaded at the kerbside, across the public footpath or in a manner which obstructs vehicular access to the site.							✓
E23	FLOOD EMERGENCY RESPONSE PLAN The Flood Emergency Response Plan required by condition D40 shall be effectively updated and maintained by the applicant.							✓
ADVISORY NOTES								
AN1	APPEALS The Applicant has the right to appeal to the Land and Environment Court in the manner set out in the EP&A Act and the EP&A Regulation.	As required	As required	As required	As required	As required	As required	As required
AN2	LONG SERVICE LEVY For work costing \$250,000 or more, a Long Service Levy must be paid. For further information, please contact the Long Service Payments Corporation Helpline on telephone 131 441.	✓						
AN3	OTHER APPROVALS AND PERMITS The Applicant shall apply to Council or other relevant authority for all necessary permits, including crane permits, road opening permits, stormwater drainage, footpaths, kerb and gutter, street trees, street lighting and signage, hoarding or scaffolding permits, footpath occupation permits and/or any other approvals under section 68 (Approvals) of the Local Government Act 1993 or section 138 of the Roads Act 1993.	As required	As required	As required	As required	As required	As required	As required
AN4	RESPONSIBILITY FOR OTHER CONSENTS / AGREEMENTS The Applicant is solely responsible for ensuring that all additional consents and agreements are obtained from other authorities, as relevant.	As required	As required	As required	As required	As required	As required	As required
AN5	TEMPORARY STRUCTURES (a) An approval under State Environmental Planning Policy (Miscellaneous Consent Provisions) 2007 must be obtained from the Authority for the erection of the temporary structures. The application must be supported by a report detailing compliance with the provisions of the NCC. (b) Structural certification from an appropriately qualified practicing structural engineer must be submitted to the Authority with the application under State Environmental Planning Policy (Miscellaneous Consent Provisions) 2007 to certify the structural adequacy of the design of the temporary structures.	As required	As required	As required	As required	As required	As required	As required
AN6	DISABILITY DISCRIMINATION ACT This application has been assessed in accordance with the EP&A Act. No guarantee is given that the proposal complies with the Disability Discrimination Act 1992. The Applicant/owner is responsible to ensure compliance with this and other anti-discrimination legislation. The Disability Discrimination Act 1992 covers disabilities not catered for in the minimum standards called up in the NCC which references AS 1428.1 - Design for Access and Mobility. AS1428 Parts 2, 3 & 4 provides the most comprehensive technical guidance under the Disability Discrimination Act 1992 currently available in Australia.	As required	As required	As required	As required	As required	As required	As required

City Campus Student Accommodation
SSDA Conditions of Consent Responsibility Matrix

[illegible]

8.2 Construction Programme

Line	Unique task ID	Name	Duration	Start	Finish	Predecessors	2025												2026												2027																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																	
							F	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February	March

ProJ ref: C:\Users\MTuttle\Hansen Yuncken\SN114 UoN Student Accommodation - Documents\06 Time\6.1 Programs\1 Program - Contract\ASTA\250710 - UoNSA - Contract - EOT001 - SSDA Update 04.pr

Hansen Yuncken Sydney Corporate Park Building 1, Level 3 75-85 O'Riordan Street Alexandria NSW 2015	Programme Status: EOT001 - SSSA Delay w/ heritage delays	Programme No: SN114 - Contract - HY-PGM-0001		Issue Date: 10/07/2025
	Details of Revision Contract Program - EOT001 Update - SSSA Delays Update 10 July 2025	View: HY - UON	Revision: 2 - EOT001	Rev Date: 26/06/2025
		Filter: Task Filter	Author: MT	Pages: 3 of 30

Hansen Yuncken Sydney Corporate Park Building 1, Level 3 75-85 O'Riordan Street Alexandria NSW 2015	Programme Status: EOT001 - SSDA Delay w/ heritage delays	Programme No: SN114 - Contract - HY-PGM-0001		Issue Date: 10/07/2025
	Details of Revision	View: HY - UON	Revision: 2 - EOT001	Rev Date: 26/06/2025
	Contract Program - EOT001 Update - SSDA Delays Update 10 July 2025	Filter: Task Filter	Author: MT	Pages: 4 of 30

Hansen Yuncken Sydney Corporate Park Building 1, Level 3 75-85 O'Riordan Street Alexandria NSW 2015	Programme Status: EOT001 - SSDA Delay w/ heritage delays	Programme No: SN114 - Contract - HY-PGM-0001		Issue Date: 10/07/2025
	Details of Revision Contract Program - EOT001 Update - SSDA Delays Update 10 July 2025	View: HY - UON	Revision: 2 - EOT001	Rev Date: 26/06/2025
		Filter: Task Filter	Author: MT	Pages: 5 of 30

Line	Unique task ID	Name	Duration	Start	Finish	Predecessors	2025												2026												2027
							F	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January			
278	802932	IFC - Review and approval	20d	Thu 07/08/25	4/09/2025	802922																									
279	802912	Low level services and RLS IFC package issued for sign off	0d	Fri 05/09/25	5/09/2025	802932																									
280	802942	Architectural / Interior Design	60d	Fri 06/06/25	5/09/2025																										
281	802943	Waterproofing	60d	Fri 06/06/25	5/09/2025																										
282	804172	IFA - Coordination, review and approval	40d	Fri 06/06/25	6/08/2025	801964																									
283	804182	IFC - Review and approval	20d	Thu 07/08/25	4/09/2025	804172																									
284	803052	Waterproofing IFC package issued for sign off	0d	Fri 05/09/25	5/09/2025	804182																									
285	803182	Floor finishes	60d	Fri 06/06/25	5/09/2025																										
286	804192	IFA - Coordination, review and approval	40d	Fri 06/06/25	6/08/2025	801964																									
287	804202	IFC - Review and approval	20d	Thu 07/08/25	4/09/2025	804192																									
288	803192	Floor finishes IFC package issued for sign off	0d	Fri 05/09/25	5/09/2025	804202																									
289	803142	Wall finishes	60d	Fri 06/06/25	5/09/2025																										
290	804212	IFA - Coordination, review and approval	40d	Fri 06/06/25	6/08/2025	801964																									
291	804222	IFC - Review and approval	20d	Thu 07/08/25	4/09/2025	804212																									
292	803152	Wall finishes IFC package issued for sign off	0d	Fri 05/09/25	5/09/2025	804222																									
293	803102	Doors, door frames and door hardware	60d	Fri 06/06/25	5/09/2025																										
294	804232	IFA - Coordination, review and approval	40d	Fri 06/06/25	6/08/2025	801964																									
295	804242	IFC - Review and approval	20d	Thu 07/08/25	4/09/2025	804232																									
296	803112	Doors, door frames and door hardware IFC package issued for sign off	0d	Fri 05/09/25	5/09/2025	804242																									
297	803062	Joinery	60d	Fri 06/06/25	5/09/2025																										
298	804252	IFA - Coordination, review and approval	40d	Fri 06/06/25	6/08/2025	801964																									
299	804262	IFC - Review and approval	20d	Thu 07/08/25	4/09/2025	804252																									
300	803072	Joinery IFC package issued for sign off	0d	Fri 05/09/25	5/09/2025	804262																									
301	803022	FFE	60d	Fri 06/06/25	5/09/2025																										
302	804272	IFA - Coordination, review and approval	40d	Fri 06/06/25	6/08/2025	801964																									
303	804282	IFC - Review and approval	20d	Thu 07/08/25	4/09/2025	804272																									
304	803082	FFE IFC package issued for sign off	0d	Fri 05/09/25	5/09/2025	804282																									
305	802982	Signage	60d	Fri 06/06/25	5/09/2025																										
306	804292	IFA - Coordination, review and approval	40d	Fri 06/06/25	6/08/2025	801964																									
307	804302	IFC - Review and approval	20d	Thu 07/08/25	4/09/2025	804292																									
308	803092	Waterproofing IFC package issued for sign off	0d	Fri 05/09/25	5/09/2025	804302																									
309	803222	Bathroom	60d	Fri 06/06/25	5/09/2025																										
310	804312	IFA - Coordination, review and approval	40d	Fri 06/06/25	6/08/2025	801964																									
311	804322	IFC - Review and approval	20d	Thu 07/08/25	4/09/2025	804312																									
312	803232	Bathroom IFC package issued for sign off	0d	Fri 05/09/25	5/09/2025	804322																									
313	802842	100% Design IFC Review & Sign off	10d	Fri 05/09/25	19/09/2025																										
314	802872	PACKAGE 4 - 100% Design Stakeholder & Peer Review & Sign off	10d	Fri 05/09/25	18/09/2025	802776, 802882, 802912, 803052, 803192, 803152, 803112, 803072, 803082, 803092, 803232																									
315	803982	PACKAGE 4 - Design finalisation workshop	1d	Fri 05/09/25	5/09/2025	802872																									
316	802862	PACKAGE 4 - 100% Design Complete	0d	Fri 19/09/25	19/09/2025	802872, 803982																									
317	802852	PACKAGE 4 - IFC Documents Complete & Issue to Site / Relevant Parties	0d	Fri 19/09/25	19/09/2025	802872																									
318	802782	CC4: SERVICES AND FINISHES	26d	Fri 19/09/25	27/10/2025																										
319	802792	CC4 - Submit CC4 Design & Consultants Reports	1d	Fri 19/09/25	19/09/2025	802872, 802862, 802852																									
320	802812	CC4 - PCA Review & Approval Period	15d	Mon 22/09/25	13/10/2025	802792																									
321	802822	CC4 - Finalise Documentation Following PCA Review	10d	Mon 13/10/25	24/10/2025	802812																									
322	802832	CC4 - Upload to Portal	1d	Mon 27/10/25	27/10/2025	802822																									
323	802802	CC4 - Approved (Services and finishes)	0d	Mon 27/10/25	27/10/2025	802832																									
324	803272	PACKAGE 5: BALANCE OF WORKS	59d	Fri 05/09/25	4/12/2025																										
325	803282	DESIGN DEVELOPMENT - BALANCE OF WORKS	40d	Fri 05/09/25	6/11/2025																										
326	803352	Landscape - Public domain hardscape and softscape	30d	Fri 05/09/25	22/10/2025																										
327	803602	IFA - Coordination, review and approval	20d	Fri 05/09/25	3/10/2025	802872																									
328	803612	IFC - Review and approval	10d	Wed 08/10/25	21/10/2025	803602																									
329	803492	Landscape IFC package issued for sign off	0d	Wed 22/10/25	22/10/2025	803612																									
330	803292	Landscape - Level 1 terrace hardscape and softscape	30d	Fri 05/09/25	22/10/2025																										
331	803852	IFA - Coordination, review and approval	20d	Fri 05/09/25	3/10/2025	802872																									

Hansen Yuncken Sydney Corporate Park Building 1, Level 3 75-85 O'Riordan Street Alexandria NSW 2015	Programme Status: EOT001 - SSDA Delay w/ heritage delays		Programme No: SN114 - Contract - HY-PGM-0001		Issue Date: 10/07/2025	
	Details of Revision		View: HY - UON		Revision: 2 - EOT001	
	Contract Program - EOT001 Update - SSDA Delays Update 10 July 2025		Filter: Task Filter		Rev Date: 26/06/2025	
					Author: MT	
				Pages: 6 of 30		

Line	Unique task ID	Name	Duration	Start	Finish	Predecessors	2025												2026												2027																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																
							F	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																		
332	803862	IFC - Review and approval	10d	Wed 08/10/25	21/10/2025	803852		17	17	31	14	28	12	26	9	23	17	21	4	18	1	15	29	13	27	10	24	8	5	19	12	16	2	16	30	13	27	11	25	8	22	6	20	13	17	31	14	28	12	26	9	23	17	4	18	1	15	29	13	27	10	24	8	5	19	12	16	2	16	30	13	27	11	25	8	22	6	20	13	17	31	14	28	12	26	9	23	17	4	18	1	15	29	13	27	10	24	8	5	19	12	16	2	16	30	13	27	11	25	8	22	6	20	13	17	31	14	28	12	26	9	23	17	4	18	1	15	29	13	27	10	24	8	5	19	12	16	2	16	30	13	27	11	25	8	22	6	20	13	17	31	14	28	12	26	9	23	17	4	18	1	15	29	13	27	10	24	8	5	19	12	16	2	16	30	13	27	11	25	8	22	6	20	13	17	31	14	28	12	26	9	23	17	4	18	1	15	29	13	27	10	24	8	5	19	12	16	2	16	30	13	27	11	25	8	22	6	20	13	17	31	14	28	12	26	9	23	17	4	18	1	15	29	13	27	10	24	8	5	19	12	16	2	16	30	13	27	11	25	8	22	6	20	13	17	31	14	28	12	26	9	23	17	4	18	1	15	29	13	27	10	24	8	5	19	12	16	2	16	30	13	27	11	25	8	22	6	20	13	17	31	14	28	12	26	9	23	17	4	18	1	15	29	13	27	10	24	8	5	19	12	16	2	16	30	13	27	11	25	8	22	6	20	13	17	31	14	28	12	26	9	23	17	4	18	1	15	29	13	27	10	24	8	5	19	12	16	2	16	30	13	27	11	25	8	22	6	20	13	17	31	14	28	12	26	9	23	17	4	18	1	15	29	13	27	10	24	8	5	19	12	16	2	16	30	13	27	11	25	8	22	6	20	13	17	31	14	28	12	26	9	23	17	4	18	1	15	29	13	27	10	24	8	5	19	12	16	2	16	30	13	27	11	25	8	22	6	20	13	17	31	14	28	12	26	9	23	17	4	18	1	15	29	13	27	10	24	8	5	19	12	16	2	16	30	13	27	11	25	8	22	6	20	13	17	31	14	28	12	26	9	23	17	4	18	1	15	29	13	27	10	24	8	5	19	12	16	2	16	30	13	27	11	25	8	22	6	20	13	17	31	14	28	12	26	9	23	17	4	18	1	15	29	13	27	10	24	8	5	19	12	16	2	16	30	13	27	11	25	8	22	6	20	13	17	31	14	28	12	26	9	23	17	4	18	1	15	29	13	27	10	24	8	5	19	12	16	2	16	30	13	27	11	25	8	22	6	20	13	17	31	14	28	12	26	9	23	17	4	18	1	15	29	13	27	10	24	8	5	19	12	16	2	16	30	13	27	11	25	8	22	6	20	13	17	31	14	28	12	26	9	23	17	4	18	1	15	29	13	27	10	24	8	5	19	12	16	2	16	30	13	27	11	25	8	22	6	20	13	17	31	14	28	12	26	9	23	17	4	18	1	15	29	13	27	10	24	8	5	19	12	16	2	16	30	13	27	11	25	8	22	6	20	13	17	31	14	28	12	26	9	23	17	4	18	1	15	29	13	27	10	24	8	5	19	12	16	2	16	30	13	27	11	25	8	22	6	20	13	17	31	14	28	12	26	9	23	17	4	18	1	15	29	13	27	10	24	8	5	19	12	16	2	16	30	13	27	11	25	8	22	6	20	13	17	31	14	28	12	26	9	23	17	4	18	1	15	29	13	27	10	24	8	5	19	12	16	2	16	30	13	27	11	25	8	22	6	20	13	17	31	14	28	12	26	9	23	17	4	18	1	15	29	13	27	10	24	8	5	19	12	16	2	16	30	13	27	11	25	8	22	6	20	13	17	31	14	28	12	26	9	23	17	4	18	1	15	29	13	27	10	24	8	5	19	12	16	2	16	30	13	27	11	25	8	22	6	20	13	17	31	14	28	12	26	9	23	17	4	18	1	15	29	13	27	10	24	8	5	19	12	16	2	16	30	13	27	11	25	8	22	6	20	13	17	31	14	28	12	26	9	23	17	4	18	1	15	29	13	27	10	24	8	5	19	12	16	2	16	30	13	27	11	25	8	22	6	20	13	17	31	14	28	12	26	9	23	17	4	18	1	15	29	13	27	10	24	8	5	19	12	16	2	16	30	13	27	11	25	8	22	6	20	13	17	31	14	28	12	26	9	23	17	4	18	1	15	29	13	27	10	24	8	5	19	12	16	2	16	30	13	27	11	25	8	22	6	20	13	17	31	14	28	12	26	9	23	17	4	18	1	15	29	13	27	10	24	8	5	19	12	16	2	16	30	13	27	11	25	8	22	6	20	13	17	31	14	28	12	26	9	23	17	4	18	1	15	29	13	27	10	24	8	5	19	12	16	2	16	30	13	27	11	25	8	22	6	20	13	17	31	14	28	12	26	9	23	17	4	18	1	15	29	13	27	10	24	8	5	19	12	16	2	16	30	13	27	11	25	8	22	6	20	13	17	31	14	28	12	26	9	23	17	4	18	1	15	29	13	27	10	24	8	5	19	12	16	2	16	30	13	27	11	25	8	22	6	20	13	17	31	14	28	12	26	9	23	17	4	18	1	15	29	13	27	10	24	8	5	19	12	16	2	16	30	13	27	11	25	8	22	6	20	13	17	31	14	28	12	26	9	23	17	4	18	1	15	29	13	27	10	24	8	5	19	12	16	2	16	30	13	27	11	25	8	22	6	20	13	17	31	14	28	12	26	9	23	17	4	18	1	15	29	13	27	10	24	8	5	19	12	16	2	16	30	13	27	11	25	8	22	6	20	13	17	31	14	28	12	26	9	23	17	4	18	1	15	29	13	27	10	24	8	5	19	12	16	2	16	30	13	27	11	25	8	22	6	20	13	17	31	14	28	12	26	9	23	17	4	18	1	15	29	13	27	10	24	8	5	19	12	16	2	16	30	13	27	11	25	8	22	6	20	13	17	31	14	28	12	26	9	23	17	4	18	1	15	29	13	27	10	24	8	5	19	12	16	2	16	30	13	27	11	25	8	22	6	20	13	17	31	14	28	12	26	9	23	17	4	18	1	15	29	13	27	10	24	8	5	19	12	16	2	16	30	13	27	11	25	8	22	6	20	13	17	31	14	28	12	26	9	23	17	4	18	1	15	29	13	27	10	24	8	5	19	12	16	2	16	30	13	27	11	25	8	22	6	20	13	17	31	14	28	12	26	9	23	17	4	18	1	15	29	13	27	10	24	8	5	19	12	16	2	16	30	13	27	11	25	8	22	6	20	13	17	31	14	28	12	26	9	23	17	4	18	1	15	29	13	27	10	24	8	5	19	12	16	2	16	30	13	27	11	25	8	22	6	20	13	17	31	14	28	12	26	9	23	17	4	18	1	15	29	13	27	10	24	8	5	19	12	16	2	16	30	13	27	11	25	8	22	6	20	13	17	31	14	28	12	26	9	23	17	4	18	1	15	29	13	27	10	24	8	5	19	12	16	2	16	30	13	27	11	25	8	22	6	20	13	17	31	14	28	12	26	9	23	17	4	18	1	15	29	13	27	10	24	8	5	19	12	16	2	16	30	13	27	11	25	8	22	6	20	13	17	31	14	28	12	26	9	23	17	4	18	1	15	29	13	27	10	24	8	5	19	12	16	2	16	30	13	27	11	25	8

Line	Unique task ID	Name	Duration	Start	Finish	Predecessors	2025												2026												2027																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																															
							F	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	F																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																	
390	792122	Pods Pacakage Awarded	0d	Thu 01/05/25	1/05/2025	792072		17	17	31	14	28	12	26	9	23	7	21	4	18	1	15	29	13	27	10	24	8	5	19	2	16	10	24	18	1																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																										
391	1766	CURTAIN WALL	30d	Mon 17/03/25	1/05/2025			-3	-1	1	3	15	7	9	11	13	15	17	19	21	23	25	27	29	31	33	35	37	39	43	45	47	49	51	53	55	57	59	61	63	65	67	69	71	73	75	77	79	81	83	85	87	89	91	93	95	97																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																					
392	1767	Curtain Wall - Tender update and resubmission	10d	Mon 17/03/25	28/03/2025	784522																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																								

Hansen Yuncken Sydney Corporate Park Building 1, Level 3 75-85 O'Riordan Street Alexandria NSW 2015	Programme Status: EOT001 - SSDA Delay w/ heritage delays		Programme No: SN114 - Contract - HY-PGM-0001		Issue Date: 10/07/2025	
	Details of Revision		View: HY - UON		Revision: 2 - EOT001	
	Contract Program - EOT001 Update - SSDA Delays Update 10 July 2025		Filter: Task Filter		Rev Date: 26/06/2025	
			Author: MT		Pages: 8 of 30	

Line	Unique task ID	Name	Duration	Start	Finish	Predecessors	2025																							
							F	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February	March
448	1800	Finish	0d	Mon 13/07/26	13/07/2026	1849	17	17	31	14	28	12	26	9	23	7	21	4	18	1	15	29	13	27	10	24	8	5	19	2
449	1801	GROUNDWORKS	56d	Wed 13/08/25	6/11/2025		18	1	3	15	7	9	11	13	15	17	19	21	23	25	27	29	31	33	35	37	39	43	45	47
450	1802	Start	0d	Wed 13/08/25	13/08/2025	1825																								
451	1803	Finish	0d	Thu 06/11/25	6/11/2025	1834																								
452	1804	STRUCTURE (CONCRETE)	159d	Tue 23/09/25	2/06/2026																									
453	1805	Start	0d	Tue 23/09/25	23/09/2025	1853																								
454	1806	Finish	0d	Tue 02/06/26	2/06/2026	1990, 1988																								
455	1807	FAÇADE	130d	Mon 09/03/26	23/09/2026																									
456	1808	Start	0d	Mon 09/03/26	9/03/2026	800882																								
457	1809	Finish	0d	Wed 23/09/26	23/09/2026	2061																								
458	1810	FIT OUT	173d	Tue 24/02/26	12/11/2026																									
459	1811	Start	0d	Tue 24/02/26	24/02/2026	2070																								
460	1812	Finish	0d	Thu 12/11/26	12/11/2026	2369, 2070																								
461	1813	COMMISSIONING / HANDOVER	15d	Thu 05/11/26	26/11/2026																									
462	1814	Start	0d	Thu 05/11/26	5/11/2026	2416																								
463	1815	Finish	0d	Thu 26/11/26	26/11/2026	2422																								
464	1816	ON SITE WORKS	356d	Thu 03/07/25	12/01/2027																									
465	1817	SITE ESTABLISHMENT	318d	Thu 03/07/25	5/11/2026																									
466	1818	Commence Works on Site (Enabling Works by Others Complete)	0d	Thu 03/07/25	3/07/2025	1652, 1740, 1742, 800653, 791772																								
467	1819	Establish Temporary Hoardings & Fencing	5d	Fri 04/07/25	10/07/2025	1818																								
468	1820	Establish Temp. Site Accommodation & Amenities + Construction Access Paths	10d	Fri 11/07/25	24/07/2025	1819																								
469	1821	Set-up Environmental Controls & Sediment Basin	5d	Fri 11/07/25	17/07/2025	1819																								
470	1822	Establish Vehicular Access / Loading Zones	5d	Fri 25/07/25	1/08/2025	1820																								
471	1823	Site Establishment Complete	0d	Fri 01/08/25	1/08/2025	1746, 1747, 1819, 1820, 1821, 1822																								
472	1824	GROUNDWORKS	56d	Wed 13/08/25	6/11/2025																									
473	1825	Strip & Clear Site Top Soil & Remaining Vegetation	1d	Wed 13/08/25	13/08/2025	1823, 802642, 1663, 792632																								
474	1826	Survey & Set out	1d	Thu 14/08/25	14/08/2025	1825																								
475	1827	Install Temporary Shoring to Facilitate Bulk Earthworks (Mainly Property Boundaries)	5d	Fri 15/08/25	22/08/2025	1826																								
476	1828	Bulk Earthworks (Cut & Fill / Batter) to Working Levels	2d	Mon 25/08/25	26/08/2025	1825, 1827																								
477	1829	Proof Roll / Prepare Building & Piling Platform	10d	Wed 27/08/25	9/09/2025	1828																								
478	1830	Install Foundation Piles / Trim to Length (West - Pour 1 Footprint)	15d	Wed 10/09/25	1/10/2025	1829, 792205																								
479	1831	Acid Sulphate Soil Remediation	22d	Wed 17/09/25	21/10/2025	1830																								
480	1832	Load out Pile Spoil	10d	Wed 22/10/25	5/11/2025	1831																								
481	1833	Install Foundation Piles / Trim to Length (East - Pour 2 Footprint)	10d	Thu 02/10/25	17/10/2025	1830																								
482	1834	Groundworks Complete	0d	Thu 06/11/25	6/11/2025	1832, 1833																								
483	1835	MATERIALS HANDLING	242d	Wed 24/09/25	7/10/2026																									
484	1836	TOWER CRANE	231d	Wed 24/09/25	17/09/2026																									
485	1837	Tower Crane - Construct Crane Base / Cure	15d	Wed 24/09/25	16/10/2025	1829, 1830, 792692																								
486	1838	Tower Crane - Erect Crane	1d	Fri 17/10/25	17/10/2025	1837																								
487	1839	Tower Crane - Crane Removal (Building Loaded Out)	1d	Thu 17/09/26	17/09/2026	1838, 2366, 1846, 794772																								
488	1840	HOIST	161d	Wed 04/02/26	7/10/2026																									
489	1841	Hoist - Erect Hoist (Level 3 Poured)	3d	Wed 04/02/26	6/02/2026	790882																								
490	1842	Hoist - Remove Hoist (Builder's Lift Available)	3d	Wed 02/09/26	4/09/2026	1841, 2067																								
491	1843	Hoist - Make Good Façade & Hoist Affected Areas / Complete Remaining Finishes	20d	Mon 07/09/26	7/10/2026	1842																								
492	794752	LOADING BAYS	113d	Mon 30/03/26	17/09/2026																									
493	794753	L2 P1 - Loading Bay Install	1d	Mon 30/03/26	30/03/2026	2010																								
494	794772	Loading Bay - Removal of Last Bay	0d	Thu 17/09/26	17/09/2026																									
495	1844	SCAFFOLD (GF TO L3)	0d	Tue 11/11/25	11/11/2025																									
496	1845	Scaffold - Commence Scaffold Erection	0d	Tue 11/11/25	11/11/2025	1877																								
497	1846	Scaffold - Removed	0d	Tue 11/11/25	11/11/2025	1845																								
498	1847	SCREENS	138d	Fri 05/12/25	13/07/2026																									
499	1848	Screens - Commence Screen Erection	0d	Fri 05/12/25	5/12/2025	1938																								
500	1849	Screens - Removed	0d	Mon 13/07/26	13/07/2026	1848, 2058																								
501	1850	STRUCTURE	191d	Tue 23/09/25	20/07/2026																									
502	1851	LIFT PIT (2.9m DEEP)	16d	Tue 23/09/25	16/10/2025																									
503	1853	Lift Pit - Detail Excavate to Core Base (1.4m Lift Shaft + 1.0m Core Base)	1d	Tue 23/09/25	23/09/2025	1830, 1757																								
504	792692	CFA breakback required -	4d	Wed 24/09/25	29/09/2025	1853																								

Hansen Yuncken Sydney Corporate Park Building 1, Level 3 75-85 O'Riordan Street Alexandria NSW 2015	Programme Status: EOT001 - SSDA Delay w/ heritage delays		Programme No: SN114 - Contract - HY-PGM-0001		Issue Date: 10/07/2025	
	Details of Revision		View: HY - UON		Revision: 2 - EOT001	
	Contract Program - EOT001 Update - SSDA Delays Update 10 July 2025		Filter: Task Filter		Author: MT	
					Rev Date: 26/06/2025	
					Pages: 9 of 30	

Hansen Yuncken Sydney Corporate Park Building 1, Level 3 75-85 O'Riordan Street Alexandria NSW 2015	Programme Status: EOT001 - SSDA Delay w/ heritage delays	Programme No: SN114 - Contract - HY-PGM-0001		Issue Date: 10/07/2025
	Details of Revision Contract Program - EOT001 Update - SSDA Delays Update 10 July 2025	View: HY - UON	Revision: 2 - EOT001	Rev Date: 26/06/2025
		Filter: Task Filter	Author: MT	Pages: 10 of 30

Proj ref: C:\Users\MTuttle\Hansen Yuncken\SN114 UoN Student Accommodation - Documents\06 Time\6.1 Programs\1 Program - Contract\ASTA\250710 - UoNSA - Contract - EOT001 - SSSA Update 04.pr

Hansen Yuncken Sydney Corporate Park Building 1, Level 3 75-85 O'Riordan Street Alexandria NSW 2015	Programme Status: EOT001 - SSDA Delay w/ heritage delays		Programme No: SN114 - Contract - HY-PGM-0001		Issue Date: 10/07/2025
	Details of Revision Contract Program - EOT001 Update - SSDA Delays Update 10 July 2025		View: HY - UON	Revision: 2 - EOT001	Rev Date: 26/06/2025
			Filter: Task Filter	Author: MT	Pages: 12 of 30

Line	Unique task ID	Name	Duration	Start	Finish	Predecessors	2025												2026												2027																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																													
							F	M	A	M	J	J	A	S	O	N	J	F	M	A	M	J	J	A	S	O	N	J	F																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																															
							17	17	31	14	28	12	26	9	23	7	9	11	13	15	17	19	21	23	25	27	29	31	33	35	37	39	41	43	45	47	49	51	53	55	57	59	61	63	65	67	69	71	73	75	77	79	81	83	85	87	89	91	93	95	97																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																															
678	794342	Pour Stairs	1d	Mon 09/03/26	9/03/2026	794332																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																						

Hansen Yuncken Sydney Corporate Park Building 1, Level 3 75-85 O'Riordan Street Alexandria NSW 2015	Programme Status: EOT001 - SSDA Delay w/ heritage delays		Programme No: SN114 - Contract - HY-PGM-0001		Issue Date: 10/07/2025	
	Details of Revision		View: HY - UON		Revision: 2 - EOT001	
	Contract Program - EOT001 Update - SSDA Delays Update 10 July 2025		Filter: Task Filter		Author: MT	
					Rev Date: 26/06/2025	Pages: 13 of 30

Proj ref: C:\Users\MTuttle\Hansen Yuncken\SN114 UoN Student Accommodation - Documents\06 Time\6.1 Programs\1 Program - Contract\ASTA\250710 - UoNSA - Contract - EOT001 - SSDA Update 04.pr

Line	Unique task ID	Name	Duration	Start	Finish	Predecessors	2025																							
							F	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	February	March
794	794552	Stair FRP (Stairmaster or similar)	2d	Fri 12/06/26	15/06/2026	794542																								
795	794562	Pour Stairs	1d	Tue 14/06/26	16/06/2026	794552																								
796	794622	Scaffold to Roof Structure.	1d	Wed 17/06/26	17/06/2026	794562																								
797	1988	Building Topped Out	0d	Mon 01/06/26	1/06/2026	790752, 791662																								
798	1989	ROOF OVERRUN	1d	Tue 02/06/26	2/06/2026																									
799	1990	Above Roof - Precast Lift Overruns / Lid Slab	1d	Tue 02/06/26	2/06/2026	1988, 790752																								
800	1991	STRUCTURAL STEEL (ABOVE L9 PLANT LEVEL)	5d	Fri 29/05/26	4/06/2026																									
801	1992	Roof Plant - Install Structural Steel to Plant Room (East)	5d	Fri 29/05/26	4/06/2026	1761, 1765, 791662, 800202																								
802	1994	POST TENSIONING & BACK PROPPING REMOVAL	143d	Fri 05/12/25	20/07/2026																									
803	1995	POST TENSIONING	116d	Fri 05/12/25	10/06/2026																									
804	1996	L1 P1 - Initial Stress, Final Stress & Grout	5d	Fri 05/12/25	11/12/2025	1881																								
805	786142	L1 P2 - Initial Stress, Final Stress & Grout	5d	Wed 17/12/25	23/12/2025	792582																								
806	1997	L1 P3 - Initial Stress, Grout & Final Stress (Pour 3)	5d	Fri 20/03/26	27/03/2026	1891																								
807	786162	L2 P1 - Initial Stress, Final Stress & Grout	5d	Wed 24/12/25	8/01/2026	788632																								
808	786152	L2 P2 - Initial Stress, Final Stress & Grout	5d	Wed 14/01/26	20/01/2026	788802																								
809	1998	L3 P1 - Initial Stress, Final Stress & Grout	5d	Wed 21/01/26	29/01/2026	1996, 789492																								
810	786172	L3 P2 - Initial Stress, Final Stress & Grout	5d	Wed 04/02/26	10/02/2026	790882																								
811	1999	L4 P1 - Initial Stress, Final Stress & Grout	5d	Wed 11/02/26	17/02/2026	1998, 789672																								
812	786182	L4 P2 - Initial Stress, Final Stress & Grout	5d	Tue 24/02/26	2/03/2026	791012																								
813	2000	L5 P1 - Initial Stress, Final Stress & Grout	5d	Tue 03/03/26	9/03/2026	1999, 789852																								
814	786192	L5 P2 - Initial Stress, Final Stress & Grout	5d	Fri 13/03/26	19/03/2026	791142																								
815	2001	L6 P1 - Initial Stress, Final Stress & Grout	5d	Fri 20/03/26	27/03/2026	2000, 790032																								
816	786202	L6 P2 - Initial Stress, Final Stress & Grout	5d	Thu 02/04/26	13/04/2026	791272																								
817	2002	L7 P1 - Initial Stress, Final Stress & Grout	5d	Tue 14/04/26	20/04/2026	2001, 790212																								
818	786212	L7 P2 - Initial Stress, Final Stress & Grout	5d	Fri 24/04/26	1/05/2026	791402																								
819	2003	L8 P1 - Initial Stress, Final Stress & Grout	5d	Mon 04/05/26	8/05/2026	2002, 790392																								
820	786222	L8 P2 - Initial Stress, Final Stress & Grout	5d	Tue 12/05/26	19/05/2026	791532																								
821	2004	L9 P1 (Plant Level) - Initial Stress, Final Stress & Grout	5d	Thu 21/05/26	27/05/2026	2003, 790572																								
822	786232	L9 P2 - Initial Stress, Final Stress & Grout	5d	Tue 26/05/26	1/06/2026	791662																								
823	2005	L10 (Roof Plant) - Initial Stress, Grout & Final Stress (Pour 1 & 2)	5d	Tue 02/06/26	10/06/2026	2004, 790752																								
824	2006	BACK PROPPING REMOVAL	99d	Wed 18/02/26	20/07/2026																									
825	2007	GF - u/s L1 P1- Strip Formwork & Remove Back props	3d	Wed 18/02/26	20/02/2026	786162, 1999																								
826	786242	GF - u/s L1 P2- Strip Formwork & Remove Back props	3d	Tue 03/03/26	5/03/2026	786182, 786152																								
827	2008	GF - u/s L1 P3- Strip Formwork & Remove Back props	3d	Wed 15/04/26	17/04/2026	1997																								
828	2009	L1 P1 - u/s L2 P1- Strip Formwork & Remove Back props	3d	Tue 10/03/26	12/03/2026	786162, 2000																								
829	786252	L1 P2 - u/s L2 P2- Strip Formwork & Remove Back props	3d	Fri 20/03/26	25/03/2026	786192																								
830	2010	L2 P1 - u/s L3 P1- Strip Formwork & Remove Back props	3d	Mon 30/03/26	1/04/2026	2001																								
831	788812	L2 P2 - u/s L3 P2- Strip Formwork & Remove Back props	3d	Tue 14/04/26	16/04/2026	786202																								
832	2011	L3 P1 - u/s L4 P1- Strip Formwork & Remove Back props	3d	Tue 21/04/26	23/04/2026	2002																								
833	788822	L3 P2 - u/s L4 P2- Strip Formwork & Remove Back props	3d	Mon 04/05/26	6/05/2026	786212																								
834	2012	L4 P1 - u/s L5 P1- Strip Formwork & Remove Back props	3d	Mon 11/05/26	13/05/2026	2003																								
835	788832	L4 P2 - u/s L5 P2- Strip Formwork & Remove Back props	3d	Wed 20/05/26	22/05/2026	786222																								
836	2013	L5 P1 - u/s L6 P1- Strip Formwork & Remove Back props	3d	Thu 28/05/26	1/06/2026	2004																								
837	788892	L5 P2 - u/s L6 P2- Strip Formwork & Remove Back props	3d	Fri 05/06/26	11/06/2026	786232																								
838	2014	L6 P1 - u/s L7 P1- Strip Formwork & Remove Back props	3d	Thu 11/06/26	15/06/2026	2005																								
839	788902	L6 P2 - u/s L7 P2- Strip Formwork & Remove Back props	3d	Fri 12/06/26	16/06/2026	786232, 788892																								
840	2015	L7 P1 - u/s L8 P1- Strip Formwork & Remove Back props	3d	Thu 18/06/26	22/06/2026	2005, 2014																								
841	788912	L7 P2 - u/s L8 P2- Strip Formwork & Remove Back props	2d	Tue 23/06/26	24/06/2026	786232, 788902																								
842	2016	L8 P1 - u/s L9 P1- Strip Formwork & Remove Back props	3d	Thu 25/06/26	30/06/2026	788912, 2005, 2015																								
843	788922	L8 P2 - u/s L9 P2- Strip Formwork & Remove Back props	2d	Wed 01/07/26	2/07/2026	788912																								
844	2017	L9 P1- Strip Formwork & Remove Back props to Underside of L10	3d	Fri 03/07/26	7/07/2026	788922, 2005, 2016																								
845	789032	ST01 - Stair Stripping - Final Levels	4d	Thu 09/07/26	14/07/2026	794562																								
846	789042	ST01 - Drop Perimeter Scaffold	4d	Wed 15/07/26	20/07/2026	789032																								
847	2018	BUILDING ENVELOPE	140d	Tue 24/02/26	23/09/2026																									
848	2019	EXTERNAL CLADDING	140d	Tue 24/02/26	23/09/2026																									
849	2020	GROUND FLOOR	81d	Tue 24/02/26	26/06/2026																									
850	2031	WEST	16d	Tue 24/02/26	17/03/2026																									
851	800882	GF P1 - Construct External Walls (Subframes, Brackets, Claddings etc.)	10d	Tue 24/02/26	9/03/2026	2007, 802622																								

Hansen Yuncken Sydney Corporate Park Building 1, Level 3 75-85 O'Riordan Street Alexandria NSW 2015	Programme Status: EOT001 - SSDA Delay w/ heritage delays		Programme No: SN114 - Contract - HY-PGM-0001		Issue Date: 10/07/2025	
	Details of Revision		View: HY - UON		Revision: 2 - EOT001	
	Contract Program - EOT001 Update - SSDA Delays Update 10 July 2025		Filter: Task Filter		Rev Date: 26/06/2025	
			Author: MT		Pages: 15 of 30	

Line	Unique task ID	Name	Duration	Start	Finish	Predecessors	2025												2026												2027
							F	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January			
852	800892	GF P1 - Window Frames & Glazing	12d	Mon 02/03/26	17/03/2026	800882																									
853	2041	EAST	52d	Fri 06/03/26	26/05/2026																										
854	2022	GF P2 - Construct External Walls (Subframes, Brackets, Claddings etc.)	10d	Fri 06/03/26	19/03/2026	1769, 2007, 786242, 802622																									
855	2023	GF P2 - Window Frames & Glazing	12d	Thu 12/03/26	30/03/2026	2022																									
856	794722	GF P2 - Brickwork Facade to Level 1	10d	Tue 28/04/26	11/05/2026																										
857	800872	GF P2 - Window Frames & Glazing	10d	Tue 12/05/26	26/05/2026	794722																									
858	2024	POUR 3 DELAYED POUR AFFECTED ELEVATIONS (REMAINING WORKS ON NORTH)	35d	Wed 06/05/26	26/06/2026																										
859	2025	GF P3 - Construct External Walls & Brick Shopfronts (Subframes, Brackets, Claddings etc.)	30d	Wed 06/05/26	19/06/2026	2008, 1997, 800802																									
860	2026	GF P3 - Window Frames & Glazing	10d	Mon 15/06/26	26/06/2026	2025																									
861	2027	LEVEL 1	86d	Fri 13/03/26	23/07/2026																										
862	792812	L1 - P1 - Install Curtain Wall	5d	Fri 13/03/26	19/03/2026	2009, 802622, 792322																									
863	792832	L1 - P2 - Install Curtain Wall	6d	Thu 26/03/26	2/04/2026	792812, 786252																									
864	792843	Scaffold Dropped to enable start	0d	Tue 21/07/26	21/07/2026	789042																									
865	792862	L1 - ST01 - Install Curtain Wall	1d	Tue 21/07/26	21/07/2026	792812, 792832, 792843																									
866	792872	L1 - P1 - Framing & Sarking - Stick Built Systems	5d	Thu 19/03/26	26/03/2026	792812																									
867	792892	L1 - P2 - Framing & Sarking - Stick Built Systems	8d	Wed 08/04/26	17/04/2026	792872, 792832																									
868	792923	LEVEL 1 - POUR 3	31d	Wed 10/06/26	23/07/2026																										
869	792933	L1 P3 - Grouting of Pour 3 TMJ	2d	Wed 10/06/26	11/06/2026	1997																									
870	792924	L1 P3 - Waterproofing to Planters & Openings as req	5d	Fri 12/06/26	18/06/2026	800852, 792933																									
871	792925	L1 P3 - Masonry Skin Install	15d	Mon 22/06/26	13/07/2026	792924, 2025																									
872	792932	L1 P3 - Strip Scaffold	3d	Tue 14/07/26	16/07/2026	2026, 792924, 2025, 792925																									
873	800862	L1 P3 Waterproof remaining L1 Slab	5d	Fri 17/07/26	23/07/2026	792932																									
874	2030	LEVEL 2	71d	Wed 08/04/26	22/07/2026																										
875	793012	L2 - ST01 - Install Curtain Wall	1d	Wed 22/07/26	22/07/2026	792862																									
876	2033	LEVEL 3	59d	Tue 28/04/26	23/07/2026																										
877	793122	L3 - P1 - Install Curtain Wall	5d	Tue 28/04/26	4/05/2026	2011																									
878	793152	L3 - P2 - Install Curtain Wall	6d	Thu 07/05/26	14/05/2026	793122, 788822																									
879	793172	L3 - ST01 - Install Curtain Wall	1d	Thu 23/07/26	23/07/2026	793152, 793012																									
880	793192	L3 - P1 - Framing & Sarking - Stick Built Systems	5d	Tue 05/05/26	11/05/2026	793122																									
881	793212	L3 - P2 - Framing & Sarking - Stick Built Systems	8d	Fri 15/05/26	27/05/2026	793152, 793192																									
882	2036	LEVEL 4	47d	Fri 15/05/26	24/07/2026																										
883	793272	L4 - P1 - Install Curtain Wall	5d	Fri 15/05/26	22/05/2026	793122, 793122, 2012, 793152																									
884	793302	L4 - P2 - Install Curtain Wall	6d	Mon 25/05/26	1/06/2026	793272, 793152, 793152, 788832																									
885	793322	L4 - ST01 - Install Curtain Wall - Potential L1P1 South Inclusion?	1d	Fri 24/07/26	24/07/2026	793272, 793302, 793172																									
886	793342	L4 - P1 - Framing & Sarking - Stick Built Systems	5d	Fri 22/05/26	28/05/2026	793272																									
887	793362	L4 - P2 - Framing & Sarking - Stick Built Systems	10d	Tue 02/06/26	17/06/2026	793302, 793342																									
888	2039	LEVEL 5	37d	Tue 02/06/26	28/07/2026																										
889	793412	L5 - P1 - Install Curtain Wall	5d	Tue 02/06/26	10/06/2026	793272, 793272, 793272, 2013, 793302																									
890	793442	L5 - P2 - Install Curtain Wall	6d	Fri 12/06/26	19/06/2026	793412, 793302, 793302, 788892																									
891	793462	L5 - ST01 - Install Curtain Wall - Potential L1P1 South Inclusion?	1d	Tue 28/07/26	28/07/2026	793412, 793442, 793322																									
892	793482	L5 - P1 - North/PS Facade - Frame/Sark	5d	Wed 10/06/26	16/06/2026	793412																									
893	793502	L5 - P2 - East/PS Facade - Frame/Sark	10d	Mon 22/06/26	6/07/2026	793442, 793482																									
894	2042	LEVEL 6	26d	Mon 22/06/26	29/07/2026																										
895	793552	L6 - P1 - Install Curtain Wall	5d	Mon 22/06/26	26/06/2026	793412, 793412, 793412, 2014, 793442																									
896	793582	L6 - P2 - Install Curtain Wall	6d	Tue 30/06/26	7/07/2026	793552, 793442, 793442, 788902, 793552																									
897	793602	L6 - ST01 - Install Curtain Wall	1d	Wed 29/07/26	29/07/2026	793552, 793582, 793462																									
898	793622	L6 - P1 - Framing & Sarking - Stick Built Systems	5d	Fri 26/06/26	3/07/2026	793552																									
899	793642	L6 - P2 - Framing & Sarking - Stick Built Systems	8d	Wed 08/07/26	17/07/2026	793582, 793622																									
900	2045	LEVEL 7	19d	Wed 08/07/26	4/08/2026																										
901	793692	L7 - P1 - Install Curtain Wall	5d	Wed 08/07/26	14/07/2026	793552, 793552, 793552, 2015, 793582, 2058, 2058																									
902	793722	L7 - P2 - Install Curtain Wall	6d	Wed 15/07/26	22/07/2026	793692, 793582, 793582, 788912																									
903	793742	L7 - ST01 - Install Curtain Wall	1d	Thu 30/07/26	30/07/2026	793692, 793722, 793602																									
904	793762	L7 - P1 - Framing & Sarking - Stick Built Systems	5d	Tue 14/07/26	20/07/2026	793692																									

Hansen Yuncken Sydney Corporate Park Building 1, Level 3 75-85 O'Riordan Street Alexandria NSW 2015	Programme Status: EOT001 - SSDA Delay w/ heritage delays		Programme No: SN114 - Contract - HY-PGM-0001		Issue Date: 10/07/2025	
	Details of Revision		View: HY - UON		Revision: 2 - EOT001	
	Contract Program - EOT001 Update - SSDA Delays Update 10 July 2025		Filter: Task Filter		Author: MT	
					Rev Date: 26/06/2025	Pages: 16 of 30

Hansen Yuncken Sydney Corporate Park Building 1, Level 3 75-85 O'Riordan Street Alexandria NSW 2015	Programme Status: EOT001 - SSSA Delay w/ heritage delays	Programme No: SN114 - Contract - HY-PGM-0001		Issue Date: 10/07/2025
	Details of Revision Contract Program - EOT001 Update - SSSA Delays Update 10 July 2025	View: HY - UON	Revision: 2 - EOT001	Rev Date: 26/06/2025
		Filter: Task Filter	Author: MT	Pages: 17 of 30

Hansen Yuncken Sydney Corporate Park Building 1, Level 3 75-85 O'Riordan Street Alexandria NSW 2015	Programme Status: EOT001 - SSDA Delay w/ heritage delays	Programme No: SN114 - Contract - HY-PGM-0001		Issue Date: 10/07/2025
	Details of Revision	View: HY - UON	Revision: 2 - EOT001	Rev Date: 26/06/2025
	Contract Program - EOT001 Update - SSDA Delays Update 10 July 2025	Filter: Task Filter	Author: MT	Pages: 18 of 30

Hansen Yuncken Sydney Corporate Park Building 1, Level 3 75-85 O'Riordan Street Alexandria NSW 2015	Programme Status: EOT001 - SSDA Delay w/ heritage delays	Programme No: SN114 - Contract - HY-PGM-0001		Issue Date: 10/07/2025
	Details of Revision	View: HY - UON	Revision: 2 - EOT001	Rev Date: 26/06/2025
	Contract Program - EOT001 Update - SSDA Delays Update 10 July 2025	Filter: Task Filter	Author: MT	Pages: 19 of 30

Hansen Yuncken Sydney Corporate Park Building 1, Level 3 75-85 O'Riordan Street Alexandria NSW 2015	Programme Status: EOT001 - SSDA Delay w/ heritage delays	Programme No: SN114 - Contract - HY-PGM-0001		Issue Date: 10/07/2025
	Details of Revision Contract Program - EOT001 Update - SSDA Delays Update 10 July 2025	View: HY - UON	Revision: 2 - EOT001	Rev Date: 26/06/2025
		Filter: Task Filter	Author: MT	Pages: 20 of 30

Hansen Yuncken Sydney Corporate Park Building 1, Level 3 75-85 O'Riordan Street Alexandria NSW 2015	Programme Status: EOT001 - SSDA Delay w/ heritage delays	Programme No: SN114 - Contract - HY-PGM-0001		Issue Date: 10/07/2025
	Details of Revision Contract Program - EOT001 Update - SSDA Delays Update 10 July 2025	View: HY - UON	Revision: 2 - EOT001	Rev Date: 26/06/2025
		Filter: Task Filter	Author: MT	Pages: 21 of 30

Hansen Yunccken Sydney Corporate Park Building 1, Level 3 75-85 O'Riordan Street Alexandria NSW 2015	Programme Status: EOT001 - SSDA Delay w/ heritage delays	Programme No: SN114 - Contract - HY-PGM-0001		Issue Date: 10/07/2025
	Details of Revision Contract Program - EOT001 Update - SSDA Delays Update 10 July 2025	View: HY - UON	Revision: 2 - EOT001	Rev Date: 26/06/2025
		Filter: Task Filter	Author: MT	Pages: 22 of 30

Line	Unique task ID	Name	Duration	Start	Finish	Predecessors	2025												2026												2027																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																							
							F	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	F																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																									
1246	796302	L4 West - Services & Finishes Complete	0d	Mon 26/10/26	26/10/2026	796212																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																

Hansen Yuncken Sydney Corporate Park Building 1, Level 3 75-85 O'Riordan Street Alexandria NSW 2015	Programme Status: EOT001 - SSDA Delay w/ heritage delays					Programme No: SN114 - Contract - HY-PGM-0001					Issue Date: 10/07/2025				
	Details of Revision					View: HY - UON					Rev Date: 26/06/2025				
	Contract Program - EOT001 Update - SSDA Delays Update 10 July 2025					Filter: Task Filter					Pages: 23 of 30				

Project: C:\Users\MTuttle\Hansen Yuncken\SN114 UoN Student Accommodation - Documents\06 Time\6.1 Programs\1 Program - Contract\ASTA\250710 - UoNSA - Contract - EOT001 - SSDA Update 04.ppt

Hansen Yuncken Sydney Corporate Park Building 1, Level 3 75-85 O'Riordan Street Alexandria NSW 2015	Programme Status: EOT001 - SSDA Delay w/ heritage delays	Programme No: SN114 - Contract - HY-PGM-0001		Issue Date: 10/07/2025
	Details of Revision Contract Program - EOT001 Update - SSDA Delays Update 10 July 2025	View: HY - UON	Revision: 2 - EOT001	Rev Date: 26/06/2025
		Filter: Task Filter	Author: MT	Pages: 25 of 30

Line	Unique task ID	Name	Duration	Start	Finish	Predecessors	2025																							
							F	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23
1419	799362	L6 - East LB - Install Pods	1d	Thu 08/10/26	8/10/2026	799352																								
1420	799372	L6 - East LB - Soffit Rough In Completion & Sheet Remaining	2d	Thu 08/10/26	9/10/2026	799362																								
1421	799382	L6 - East LB - PB Ceiling Framing / Linings	2d	Mon 12/10/26	13/10/2026	799372																								
1422	799392	L6 - East LB - Set & Sand / Initial Paint	2d	Wed 14/10/26	15/10/2026	799382																								
1423	799402	L6 - East LB - Install Joinery, Hang Doors & Fix Hardware	3d	Fri 14/10/26	20/10/2026	799392																								
1424	799412	L6 - East LB - Kitchenettes - Joinery Installation / Services Rough in	2d	Wed 21/10/26	22/10/2026	799402																								
1425	799422	L6 - East LB - Kitchenettes - Benchtops, Sinks & Hyd. Fit-off, Splashbacks, Fittings, Etc.	3d	Fri 23/10/26	27/10/2026	799412																								
1426	799432	L6 - East LB - Resilient Floor Finishes	2d	Wed 28/10/26	29/10/2026	799422																								
1427	799442	L6 - East LB - Services Fit Off / Final Paint	2d	Wed 28/10/26	29/10/2026	799432																								
1428	799452	L6 - East LB - Lay Carpet / Install White Goods	1d	Thu 29/10/26	29/10/2026	799442																								
1429	2305	LEVEL 7 (55 UNITS)	82d	Tue 14/07/26	12/11/2026																									
1430	797362	L7 - WEST	78d	Tue 14/07/26	5/11/2026																									
1431	797762	L7 West - Delivery of Pods	1d	Tue 14/07/26	14/07/2026	793692																								
1432	797392	L7 West - High Level Services	20d	Tue 14/07/26	11/08/2026	793692																								
1433	797402	L7 West - Installation of Fire Compact Stud	5d	Wed 22/07/26	29/07/2026	797392, 797762																								
1434	797412	L7 West - Sheet, set, Sand Fire Compact	7d	Wed 05/08/26	13/08/2026	797402, 797382, 797362																								
1435	797422	L7 West - Pod Install	1d	Fri 14/08/26	14/08/2026	797402, 797412																								
1436	797432	L7 West - Frame, sheet & Set remaining partitions	6d	Fri 14/08/26	21/08/2026	797412																								
1437	797442	L7 West - PB Ceiling Framing / Linings	8d	Wed 19/08/26	31/08/2026	797432																								
1438	797452	L7 West - Set & Sand / Initial Paint	5d	Thu 27/08/26	2/09/2026	797442																								
1439	797462	L7 West - Install Joinery, Hang Doors & Fix Hardware	10d	Thu 27/08/26	9/09/2026	797452																								
1440	797472	L7 West - Kitchenettes - Joinery Installation / Services Rough in / Flooring	8d	Thu 27/08/26	7/09/2026	797452																								
1441	797482	L7 West - Kitchenettes - Benchtops, Sinks & Hyd. Fit-off, Splashbacks, Fittings, Etc.	8d	Tue 01/09/26	10/09/2026	797472																								
1442	797492	L7 West - Resilient Floor Finishes	5d	Tue 08/09/26	14/09/2026	797462																								
1443	797502	L7 West - Services Fit Off / Final Paint / Fire Stair Finishes	8d	Thu 17/09/26	29/09/2026	797462, 797482, 797492																								
1444	797512	L7 West - Lay Carpet / Install White Goods	5d	Fri 25/09/26	1/10/2026	797502																								
1445	797522	L7 West - Final Clean / Test & Commission Floor Services	5d	Fri 23/10/26	29/10/2026	797502, 797512, 799912																								
1446	797532	L7 West - Defect Inspection & Rectification	5d	Fri 30/10/26	5/11/2026	797512, 797522, 797752																								
1447	797622	L7 West - Services & Finishes Complete	0d	Thu 05/11/26	5/11/2026	797532																								
1448	797382	West - Wet Area Amenities - Insitu	23d	Thu 27/08/26	29/09/2026																									
1449	797712	L7 West - Non-Common Wet Areas - Lay Screeds & Membranes	5d	Thu 27/08/26	2/09/2026	797452																								
1450	797722	L7 West - Wet Areas - Wall & Floor Tiling	5d	Thu 03/09/26	9/09/2026	797712																								
1451	797732	L7 West - Wet Areas - Install Vanities / Hyd. Fit Off	5d	Thu 10/09/26	16/09/2026	797722																								
1452	797742	L7 West - Wet Areas - Mirrors, Shower Screens etc.	3d	Thu 17/09/26	22/09/2026	797732																								
1453	797752	L7 West - Wet Areas - Services Fit off Make Good / Filaments	5d	Wed 23/09/26	29/09/2026	797742																								
1454	2315	L7 WEST - LOADING BAY ZONE	20d	Wed 23/09/26	22/10/2026																									
1455	799812	L7 - West LB - Stud Wall & Line (Rough In Completed Earlier)	4d	Wed 23/09/26	28/09/2026	799462																								
1456	799822	L7 - West LB - Install Pods	1d	Tue 29/09/26	29/09/2026	799812																								
1457	799832	L7 - West LB - Soffit Rough In Completion & Sheet Remaining	2d	Tue 29/09/26	30/09/2026	799822																								
1458	799842	L7 - West LB - PB Ceiling Framing / Linings	2d	Thu 01/10/26	2/10/2026	799832																								
1459	799852	L7 - West LB - Set & Sand / Initial Paint	2d	Wed 07/10/26	8/10/2026	799842																								
1460	799862	L7 - West LB - Install Joinery, Hang Doors & Fix Hardware	3d	Fri 09/10/26	13/10/2026	799852																								
1461	799872	L7 - West LB - Kitchenettes - Joinery Installation / Services Rough in	2d	Wed 14/10/26	15/10/2026	799862																								
1462	799882	L7 - West LB - Kitchenettes - Benchtops, Sinks & Hyd. Fit-off, Splashbacks, Fittings, Etc.	3d	Fri 14/10/26	20/10/2026	799872																								
1463	799892	L7 - West LB - Resilient Floor Finishes	2d	Wed 21/10/26	22/10/2026	799882																								
1464	799902	L7 - West LB - Services Fit Off / Final Paint	2d	Wed 21/10/26	22/10/2026	799892																								
1465	799912	L7 - West LB - Lay Carpet / Install White Goods	1d	Thu 22/10/26	22/10/2026	799902																								
1466	797372	L7 - EAST	75d	Thu 23/07/26	12/11/2026																									
1467	797772	L7 East - Pod Delivery & Floor Storage	1d	Thu 23/07/26	23/07/2026	793722																								
1468	797542	L7 East - High Level Services	20d	Thu 23/07/26	20/08/2026	793722																								
1469	797552	L7 East - Installation of Fire Compact Stud	10d	Mon 03/08/26	14/08/2026	797402, 797542, 797772																								
1470	797562	L7 East - Sheet, set, Sand Fire Compact	10d	Fri 14/08/26	28/08/2026	797412, 797552, 793782																								
1471	797572	L7 East - Pod Install	2d	Mon 31/08/26	1/09/2026	797552, 797562																								
1472	797582	L7 East - Stud remaining & Line onside	6d	Mon 31/08/26	7/09/2026	797562																								
1473	797592	L7 East - PB Ceiling Framing / Linings	7d	Tue 08/09/26	16/09/2026	797582																								
1474	797602	L7 East - Set & Sand / Initial Paint	5d	Mon 14/09/26	18/09/2026	797592																								
1475	797632	L7 East - Install Joinery, Hang Doors & Fix Hardware	10d	Mon 14/09/26	28/09/2026	797602																								
1476	797642	L7 East - Kitchenettes - Joinery Installation / Services Rough in / Flooring	8d	Mon 14/09/26	24/09/2026	797602																								

Hansen Yuncken Sydney Corporate Park Building 1, Level 3 75-85 O'Riordan Street Alexandria NSW 2015	Programme Status: EOT001 - SSDA Delay w/ heritage delays		Programme No: SN114 - Contract - HY-PGM-0001		Issue Date: 10/07/2025	
	Details of Revision		View: HY - UON		Revision: 2 - EOT001	
	Contract Program - EOT001 Update - SSDA Delays Update 10 July 2025		Filter: Task Filter		Author: MT	
					Rev Date: 26/06/2025	
					Pages: 26 of 30	

Hansen Yuncken Sydney Corporate Park Building 1, Level 3 75-85 O'Riordan Street Alexandria NSW 2015	Programme Status: EOT001 - SSDA Delay w/ heritage delays	Programme No: SN114 - Contract - HY-PGM-0001		Issue Date: 10/07/2025
	Details of Revision Contract Program - EOT001 Update - SSDA Delays Update 10 July 2025	View: HY - UON	Revision: 2 - EOT001	Rev Date: 26/06/2025
		Filter: Task Filter	Author: MT	Pages: 27 of 30

ProJ ref: C:\Users\MTuttle\Hansen Yuncken\SN114 UoN Student Accommodation - Documents\06 Time\6.1 Programs\1 Program - Contract\ASTA\250710 - UoNSA - Contract - EOT001 - SSDA Update 04.pr

Line	Unique task ID	Name	Duration	Start	Finish	Predecessors	2025												2026												2027																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																								
							F	March	April	May	June	July	August	September	October	November	January	February	March	April	May	June	July	August	September	October	November	January	F																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																										
1593	800052	Packet/Hob Install following Facade	3d	Thu 10/09/26	14/09/2026	798092																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																	

Proj ref: C:\Users\MTuttle\Hansen Yuncken\SN114 UoN Student Accommodation - Documents\06 Time\6.1 Programs\1 Program - Contract\ASTA\250710 - UoNSA - Contract - EOT001 - SSDA Update 04.ppt
