

PLAN LIKE A PROJECT MANAGER


You're the Project Manager for a Tiny House Build. You've been given 10 days and 6 tasks. But — there's a catch!

Your challenge is to Design and build a shelter that:

- You only have 4 workers (who can do anything!)
- It's going to rain on Day 5 and 6
- Some tasks can't start until others have finished

Tasks to complete your house

- Paint and Decorate (2 days, must be last)
- Add roof (1 Day, Can't be done before walls)
- Build foundation (2 Days, Can't be done in rain)
- Order materials (Can't be done before design)
- Design the house (1 Day)
- Build Walls (2 Days)

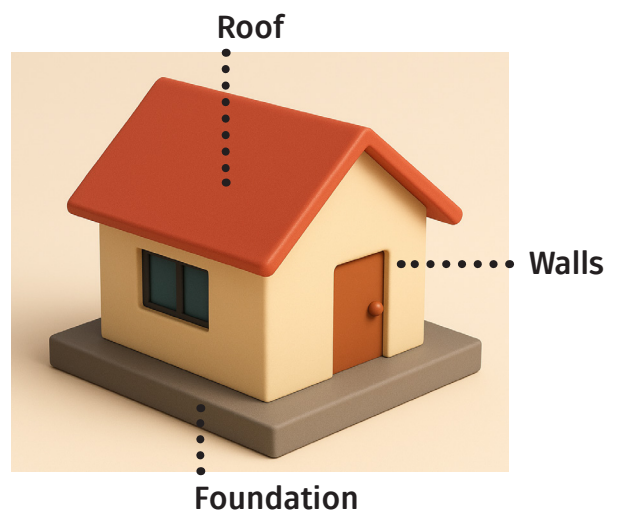

What you need to do:

- Use pencils to write the tasks onto the work plan sheet and draw the task block according to how many days the task takes
- Plan around the days of rain (Day 5 and 6)
- Assign your 4 workers - Some tasks can happen at the same time if you have enough workers!

Bonus Challenge - Can you finish everything in 8 days? What would need to change?











Reflect on what you have learnt

- Was any task hard to place because of the weather?
- How was managing both people and how long things take?
- What real-world problems did this help you understand?



UNIVERSITY OF
NEWCASTLE

STEM SPARKS

	Day 1	Day 2	Day 3	Day 4	Day 5	Day 6	Day 7	Day 8	Day 9	Day 10
Task										
Task										
Task										
Task										
Task										
Task										
Task										
Task										
Task										



UNIVERSITY OF
NEWCASTLE

STEM SPARKS

PROJECT MANAGER
